

WEEKLY REPORT OF CONSTRUCTION ACTIVITIES



Project Name: Madison Co. Bridge 502
For Week Ending: 5/18/2019
Time Elapsed: 96%
Date of Notice to Proceed: 4/28/2017
Contractor: Primco, Inc.
Owner: Madison County

Report No.: 101
Calendar Completion Date: 8/5/2019
Substantial Competition Date: 6/14/2019
Contract Amount: \$ 13,481,784.02
Incurred To Date: \$ 12,854,141.04
Designer: Beam, Longest, and Neff, LLC

Contract Number: B-36317
Project Number: 1297202
Structure Number: 502
Balance Remaining: \$ 627,642.98
Project Complete Percent: 95%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 12	No work on site.	Asphalt	Weather	0/8	No
Mon 13	Primco power washed the structure and covered the Phase 1 railing. C-Tech unloaded the ornamental and PF-1 railing.	Asphalt	Weather	0/8	No
Tues 14	E&B placed intermediate on 8th Street and the jail drive. C-Tech installed ornamental and PF-1 rail.	Asphalt	Able to work on the controlling operation	10/10	Yes
Wed 15	Custom Rock added traps and stained Spans A and B. C-Tech installed the ornamental and PF-1 rail.	Railing	Able to work on the controlling operation	8/8	Yes
Thurs 16	Custom Rock stained Span B and C. C-Tech finished the on-structure ornamental and PF-1 railing.	Railing	Able to work on the controlling operation	8/8	Yes
Fri 17	Michiana installed the remaining signal and ped poles. Custom Rock stained Span C and D. Primco power washed the Phase 1 railing.	Signal	Able to work on the controlling operation	8/8	Yes
Sat 18	Custom Rock stained Span C and D.	Signal	Able to work on the controlling operation	8/8	Yes

Distribution:

Original to Owner
 cc: Project Engineer
 cc: District File
 cc: Contractor

CONTRACTOR ACCEPTANCE

Primco, Inc.

REMARKS / PROJECTED WORK

The eastbound traffic will be switched onto the eastbound structure on Tuesday, May 21st. Primco will start replacing the Phase 1 expansion joint on Wednesday. Custom Rock Formliner will continue staining. Michiana will finish the signal and then start on the path lighting conduit and foundations.

Prepared by:

Brian Rodger

Project Engineer

Approved _____, 2019

Madison County

PROJECT PHOTOS




C-Tech installed the PF-1 rail.



E&B placed intermediate on the east end.



E&B placed intermediate on the west end.

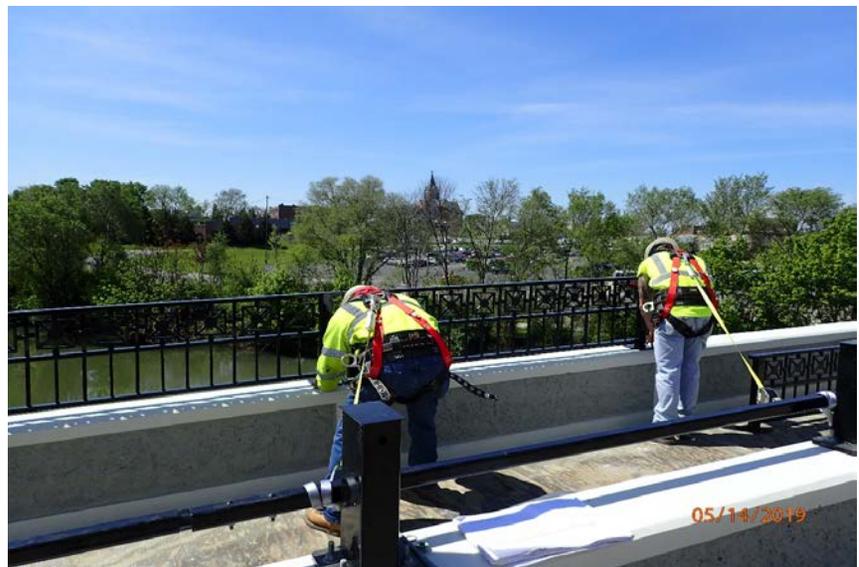

C-Tech installed the ornamental railing.

PROJECT PHOTOS



E&B paved along Wall 1.



C-Tech installed the PF-1 rail.



Custom Rock stained Pier 2.



C-Tech installed the ornamental rail.

PROJECT PHOTOS



Custom Rock stained Span B.



C-Tech installed ornamental rail at an outlook.



Michiana installed a signal pole at Central Ave.



Primco power washed the Phase 1 railing.
