



# WEEKLY REPORT OF CONSTRUCTION ACTIVITIES

**Project Name:** Madison Co. Bridge 502  
**For Week Ending:** 6/1/2019  
**Time Elapsed:** 98%  
**Date of Notice to Proceed:** 4/28/2017  
**Contractor:** Primco, Inc.  
**Owner:** Madison County

**Report No.:** 103  
**Calendar Completion Date:** 8/5/2019  
**Substantial Competition Date:** 6/14/2019  
**Contract Amount:** \$ 13,481,784.02  
**Incurred To Date:** \$ 12,993,123.15  
**Designer:** Beam, Longest, and Neff, LLC

**Contract Number:** B-36317  
**Project Number:** 1297202  
**Structure Number:** 502  
**Balance Remaining:** \$ 488,660.87  
**Project Complete Percent:** 96%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 26	No work on site.	Joint Replacement	Holiday	8/8	Yes
Mon 27	Custom Rock Formliner stained the bridge.	Joint Replacement	Holiday	8/8	Yes
Tues 28	Primco removed the Bent 7 joint and installed the new reinforcing. Custom Rock stained Wall 3. Michiana poured foundations and installed conduit for the path lighting.	Joint Replacement	Able to work on the controlling operation	8/8	Yes
Wed 29	Primco poured the Bent 7 approach and joint abutment. Custom Rock stained the railing.	Joint Replacement	Able to work on the controlling operation	8/8	Yes
Thurs 30	Primco started the Bent 1 joint removal. Custom Rock stained the railing.	Joint Replacement	Able to work on the controlling operation	7/8	Yes
Fri 31	Primco removed the Bent 1 joint. Custom Rock Formliner stained the railing.	Joint Replacement	Able to work on the controlling operation	8/8	Yes
Sat 1	Custom Rock Formliner stained Wall 7 and touched up under the bridge.	Joint Replacement	Able to work on the controlling operation	8/8	Yes

Distribution:  
 Original to Owner  
 cc: Project Engineer  
 cc: District File  
 cc: Contractor

**REMARKS / PROJECTED WORK**

NEXT WEEK: Primco will pour the Bent 1 approach and joint abutment. Custom Rock Formliner will have the staining done on Monday. 3D will fine grade and Slussers will plant the trees. C-Tech will start installing the north side ornamental rail on Tuesday.

Prepared by: Brian Rodger  
 Project Engineer

Approved \_\_\_\_\_, 2019

\_\_\_\_\_ Madison County

CONTRACTOR ACCEPTANCE

\_\_\_\_\_  
Primco, Inc.

# PROJECT PHOTOS



Primco drilled holes for the new reinforcing.



Primco poured the Bent 7 approach and joint abutment.



Primco poured the Bent 7 approach and joint abutment.



Primco removed the Bent 1 joint.

# PROJECT PHOTOS




Michiana installed conduit for the path lighting.



Custom Rock Formliner stained the bridge railing.



Staining on Wall 2 and the bridge.

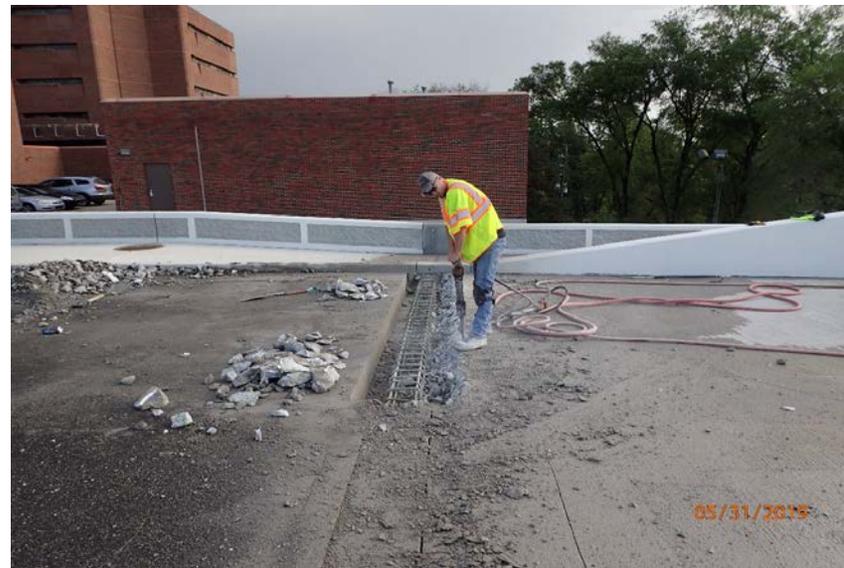

Primco removed the Bent 1 joint.
