

# WEEKLY REPORT OF CONSTRUCTION ACTIVITIES



**Project Name:** Madison Co. Bridge 502  
**For Week Ending:** 7/6/2019  
**Time Elapsed:** 99%  
**Date of Notice to Proceed:** 4/28/2017  
**Contractor:** Primco, Inc.  
**Owner:** Madison County

**Report No.:** 108  
**Calendar Completion Date:** 8/5/2019  
**Substantial Competition Date:** 6/18/2019  
**Contract Amount:** \$ 13,481,784.02  
**Incurred To Date:** \$ 13,420,232.62  
**Designer:** Beam, Longest, and Neff, LLC

**Contract Number:** B-36317  
**Project Number:** 1297202  
**Structure Number:** 502  
**Balance Remaining:** \$ 61,551.40  
**Project Complete Percent:** 99%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 30	No work on site.	Lighting	Able to work on the controlling operation	8/8	Yes
Mon 1	Slussers watered the sod and trees.	Lighting	Able to work on the controlling operation	8/8	Yes
Tues 2	Primco removed the causeway.	Lighting	Able to work on the controlling operation	8/8	Yes
Wed 3	Primco removed the causeway. Slussers watered the sod.	Lighting	Able to work on the controlling operation	4/4	Yes
Thurs 4	No work on site.	Lighting	Holiday	0/0	Yes
Fri 5	No work on site.	Lighting	Holiday	0/0	Yes
Sat 6	No work on site.	Lighting	Holiday	0/0	Yes

Distribution:  
 Original to Owner  
 cc: Project Engineer  
 cc: District File  
 cc: Contractor

**REMARKS / PROJECTED WORK**

Primco hopes to have the causeway completely removed by Friday, July 12th. The remaining section of path will be prepped on Monday, July 15th. The path light poles and all fixtures are expected to ship on July 10th. No ship date has been provided for the bridge poles.

Prepared by: Brian Rodger  
 Project Engineer

Approved \_\_\_\_\_, 2019  
 Madison County


CONTRACTOR ACCEPTANCE

\_\_\_\_\_  
Primco, Inc.

# PROJECT PHOTOS



Slussers watered the sod.

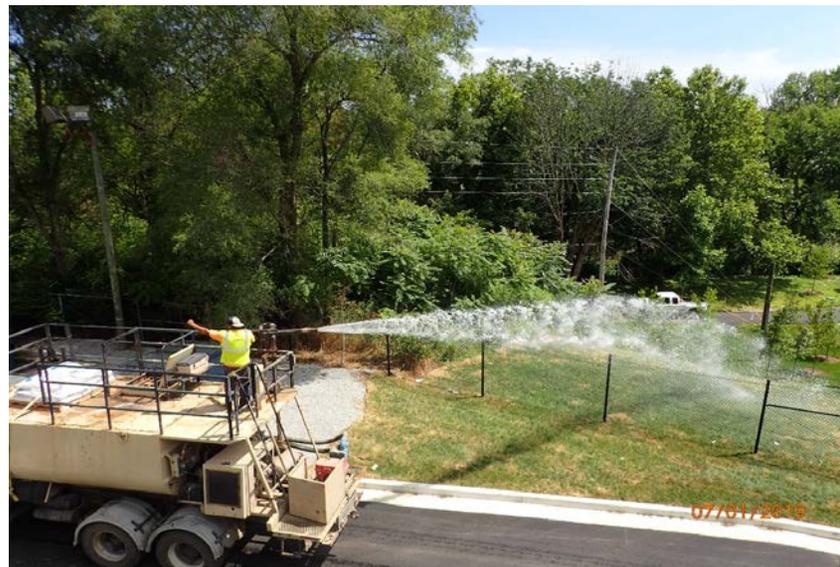

Slussers watered the sod.



Primco removed the causeway riprap.



Slussers watered the sod.
