

WEEKLY REPORT OF CONSTRUCTION ACTIVITIES



Project Name: Madison Co. Bridge 502
For Week Ending: 4/13/2019
Time Elapsed: 93%
Date of Notice to Proceed: 4/28/2017
Contractor: Primco, Inc.
Owner: Madison County

Report No.: 96
Calendar Completion Date: 8/5/2019
Substantial Competition Date: 6/14/2019
Contract Amount: \$ 13,481,784.02
Incurred To Date: \$ 12,333,208.61
Designer: Beam, Longest, and Neff, LLC

Contract Number: B-36317
Project Number: 1297202
Structure Number: 502
Balance Remaining: \$ 1,148,575.41
Project Complete Percent: 91%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 7	No work on site.	Paving	Able to work on the controlling operation	8/8	Yes
Mon 8	Primco placed the Pier 2 block mats and installed the levee wall joints. E&B placed the first lift of base on 8th Street and the jail drive.	Paving	Able to work on the controlling operation	8/8	Yes
Tues 9	Primco poured curb and gutter on the west end and installed the Pier 2 block mats.	Curb	Able to work on the controlling operation	8/8	Yes
Wed 10	Primco poured the center curb on the west end and installed the Pier 2 block mats.	Curb	Able to work on the controlling operation	5/8	Yes
Thurs 11	Primco poured the center curb on the bridge deck, placed the Pier 2 block mats, and surface sealed the sidewalk.	Curb	Able to work on the controlling operation	8/8	Yes
Fri 12	Primco poured the east end curb and gutter and placed the Pier 2 block mats.	Curb	Able to work on the controlling operation	8/8	Yes
Sat 13	No work on site.	Curb	Able to work on the controlling operation	8/8	Yes

Distribution:
 Original to Owner
 cc: Project Engineer
 cc: District File
 cc: Contractor

REMARKS / PROJECTED WORK

Primco will continue pouring the curb and gutter next week. Crews will start installing the block mats on the west river bank next week as well.

Prepared by: Brian Rodger
 Project Engineer

Approved _____, 2019

_____ Madison County

CONTRACTOR ACCEPTANCE

Primco, Inc.

PROJECT PHOTOS




E&B paved the first base lift.



Primco placed block mats on the Pier 2 slope.



E&B paved the first base lift.

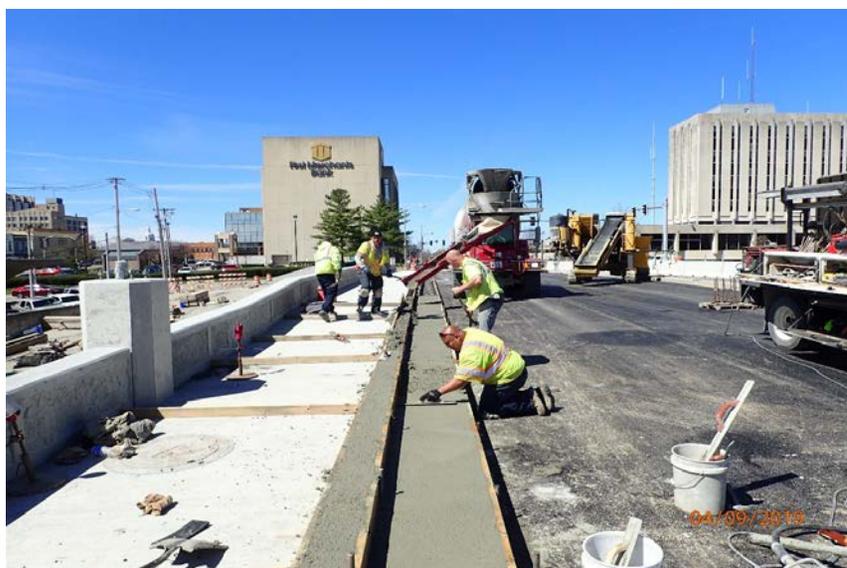

Primco poured curb and gutter.

PROJECT PHOTOS



Primco poured the center curb.



Primco installed the Pier 2 block mats.



Primco grouted the block mats and placed stone in the block voids.



Primco poured the center curb.
