



# WEEKLY REPORT OF CONSTRUCTION ACTIVITIES

**Project Name:** Madison Co. Bridge 502  
**For Week Ending:** 11/11/2017  
**Time Elapsed:** 22%  
**Date of Notice to Proceed:** 4/28/2017  
**Contractor:** Primco, Inc.  
**Owner:** Madison County

**Report No.:** 22  
**Calendar Completion Date:** 8/5/2019  
**Substantial Competition Date:** 6/5/2019  
**Contract Amount:** \$ 13,481,784.02  
**Incurred To Date:** \$ 2,189,632.21  
**Designer:** Beam, Longest, and Neff, LLC

**Contract Number:** B-36317  
**Project Number:** 1297202  
**Structure Number:** 502  
**Balance Remaining:** \$ 11,292,151.81  
**Project Complete Percent:** 16%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 5	No work on site.	Water Main Relocation	Able to work on the controlling operation	8/8	Yes
Mon 6	3D installed a construction entrance in the Athletic Field.	Water Main Relocation	Able to work on the controlling operation	8/8	Yes
Tues 7	Culy installed the MJ tapping sleeve at connection two. Two different gaskets were tried and both failed the hydrostatic testing.	Water Main Relocation	Able to work on the controlling operation	8/8	Yes
Wed 8	Culy tried another gasket at connection 2 and it failed the hydrostatic testing. 3D repaired the filter berm and removed silt.	Water Main Relocation	Able to work on the controlling operation	8/8	Yes
Thurs 9	Culy tried another gasket at connection 2 and it failed testing. Crews left at 10AM. Culy believes there is a problem with the AC main and is submitting a recommendation for the tap at connection 2.	Water Main Relocation	Able to work on the controlling operation	8/8	Yes
Fri 10	No work on site.	Water Main Relocation	Able to work on the controlling operation	8/8	Yes
Sat 11	No work on site.	Water Main Relocation	Able to work on the controlling operation	8/8	Yes

Distribution:

- Original to Owner
- cc: Project Engineer
- cc: District File
- cc: Contractor

CONTRACTOR ACCEPTANCE

\_\_\_\_\_  
Primco, Inc.

**REMARKS / PROJECTED WORK**

Due to the failed hydrostatic testing, Culy will be submitting a recommendation for tapping the existing water main at connection 2. 3D will complete the 12in water main connection for the Norton wells on Monday. Roadsafe will close the north half of the bridge on Monday, November 13th. Primco will start setting the barrier wall on November 15th and then will move on to the demolition. SJ Ludlow will perform the preconstruction survey at the jail on November 14th. AT&T is scheduled to complete the fiber cutover by November 17th. The copper lines will be pulled from the bridge by Thanksgiving.

Prepared by:

*Brian Rodgers*

\_\_\_\_\_  
Project Engineer

Approved \_\_\_\_\_, 2017

\_\_\_\_\_  
Madison County

# PROJECT PHOTOS




Culy installed the MJ tapping sleeve at connection 2.



Culy cut the gasket for the tapping sleeve.



Culy installed the tapping sleeve.

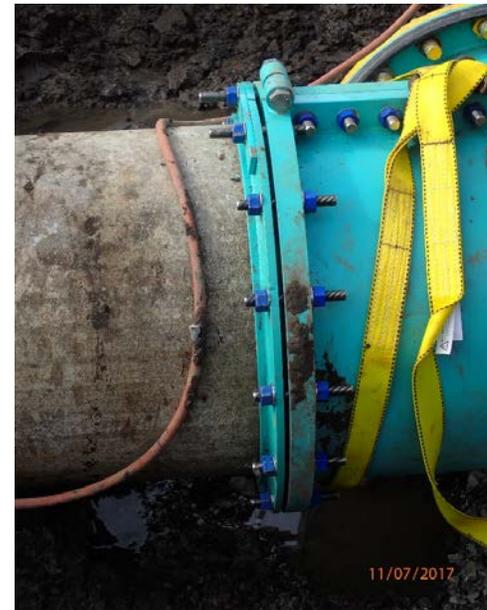

The tapping sleeve.
