

WEEKLY REPORT OF CONSTRUCTION ACTIVITIES



Project Name: Madison Co. Bridge 502
For Week Ending: 2/23/2019
Time Elapsed: 87%
Date of Notice to Proceed: 4/28/2017
Contractor: Primco, Inc.
Owner: Madison County

Report No.: 89
Calendar Completion Date: 8/5/2019
Substantial Competition Date: 6/14/2019
Contract Amount: \$ 13,481,784.02
Incurred To Date: \$ 11,816,263.05
Designer: Beam, Longest, and Neff, LLC

Contract Number: B-36317
Project Number: 1297202
Structure Number: 502
Balance Remaining: \$ 1,665,520.97
Project Complete Percent: 88%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 17	No work on site.	Wall 1 & 2	Able to work on the controlling operation	8/8	Yes
Mon 18	Primco prepped Wall 1 for CCF, tied the Bent 1 approach reinforcing, and formed the Bent 7 joint abutment.	Wall 1 & 2	Able to work on the controlling operation	8/8	Yes
Tues 19	Primco poured the Bent 7 joint abutment and tied the Bent 1 approach reinforcing. Elastizell placed CCF at Wall 1.	Wall 1 & 2	Able to work on the controlling operation	8/8	Yes
Wed 20	Primco set Wall 1 panels, poured the Bent 7 joint abutment, and placed stone at Wall 4 and Bent 7. Elastizell placed CCF at Wall 1.	Wall 1 & 2	Able to work on the controlling operation	8/8	Yes
Thurs 21	Primco placed stone for the Bent 7 approach, formed the Wall 4 moment slab, and backfilled the F.F. of Wall 1. Elastizell placed CCF at Wall 1.	Wall 1 & 2	Able to work on the controlling operation	8/8	Yes
Fri 22	Primco tied the Bent 7 approach reinforcing and prepped Bent 1. Elastizell finished the CCF at Wall 1. 3D freshened up the filter berm.	Wall 1 & 2	Able to work on the controlling operation	8/8	Yes
Sat 23	No work on site.	Wall 1 & 2	Able to work on the controlling operation	8/8	Yes

Distribution:

Original to Owner
 cc: Project Engineer
 cc: District File
 cc: Contractor

CONTRACTOR ACCEPTANCE

Primco, Inc.

REMARKS / PROJECTED WORK

Primco will pour both the Bent 1 and Bent 7 approach on Tuesday. Primco will continue working on the Wall 4 moment slab and the Wall 1 panels next week.

Prepared by:

Brian Rodger

Project Engineer

Approved _____, 2019

Madison County

PROJECT PHOTOS



Primco tied the Bent 7 joint abutment reinforcing.



Primco tied the Bent 1 approach reinforcing.




Primco poured the Bent 7 joint abutment.



Primco formed the Wall 4 moment slab.

PROJECT PHOTOS

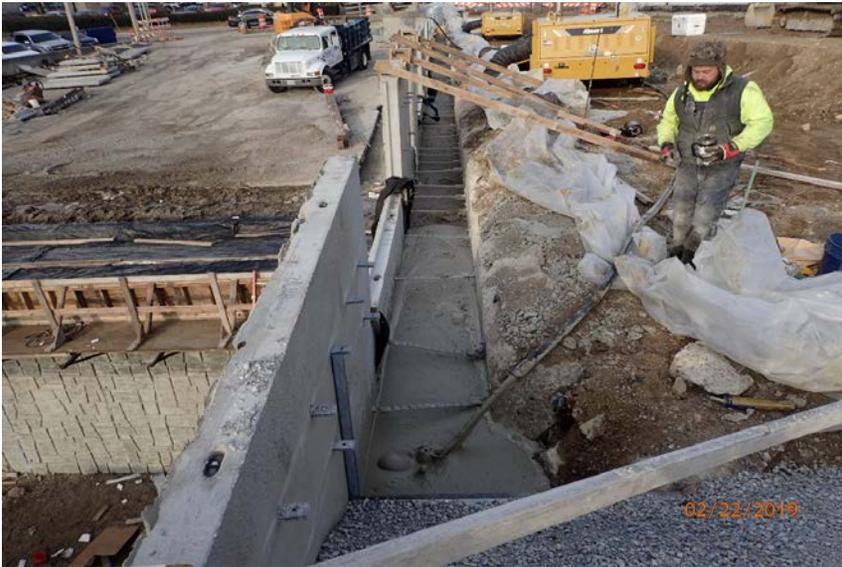

Elastzell placed the cellular concrete fill at Wall 1.



Elastzell placed the cellular concrete fill at Wall 1.



Primco tied the Bent 7 approach reinforcing.



3D freshened up the filter berm.
