

# WEEKLY REPORT OF CONSTRUCTION ACTIVITIES



**Project Name:** Madison Co. Bridge 502  
**For Week Ending:** 4/6/2019  
**Time Elapsed:** 92%  
**Date of Notice to Proceed:** 4/28/2017  
**Contractor:** Primco, Inc.  
**Owner:** Madison County

**Report No.:** 95  
**Calendar Completion Date:** 8/5/2019  
**Substantial Competition Date:** 6/14/2019  
**Contract Amount:** \$ 13,481,784.02  
**Incurred To Date:** \$ 12,217,036.99  
**Designer:** Beam, Longest, and Neff, LLC

**Contract Number:** B-36317  
**Project Number:** 1297202  
**Structure Number:** 502  
**Balance Remaining:** \$ 1,264,747.03  
**Project Complete Percent:** 91%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 31	No work on site.	Railing	Able to work on the controlling operation	8/8	Yes
Mon 1	Primco poured the Wall 1 railing transition and removed the Wall 1 jacks. 3D installed Str 18. Michiana installed signal and lighting conduit.	Railing	Able to work on the controlling operation	8/8	Yes
Tues 2	Primco poured the slopewall and the parking lot at Wall 4. 3D adjusted castings and fine graded. Michiana installed handholes and sonotubes.	Subgrade Treatment	Able to work on the controlling operation	8/8	Yes
Wed 3	Primco poured the paved side ditch and formed the slopewall.	Paving	Able to work on the controlling operation	8/8	Yes
Thurs 4	Primco poured the slopewall, the south end of Wall 4, and the parking lot at Wall 2. The bridge deck was sealed.	Paving	Able to work on the controlling operation	8/8	Yes
Fri 5	Primco placed the plank joint sealant, rubbed the bridge railing, and cleaned the site.	Paving	Able to work on the controlling operation	8/8	Yes
Sat 6	No work on site.	Paving	Able to work on the controlling operation	8/8	Yes

Distribution:  
 Original to Owner  
 cc: Project Engineer  
 cc: District File  
 cc: Contractor

**REMARKS / PROJECTED WORK**

E&B will pave the first lift of asphalt on Monday. Primco will then start pouring curb, curb ramps, sidewalk, and approaches. The center curb will be slip formed on Wednesday.

Prepared by: Brian Rodger  
 Project Engineer

Approved \_\_\_\_\_, 2019

\_\_\_\_\_ Madison County

CONTRACTOR ACCEPTANCE

\_\_\_\_\_  
Primco, Inc.


# PROJECT PHOTOS



Michiana installed the bridge lighting conduit.



Primco excavated for the slopewall toe.

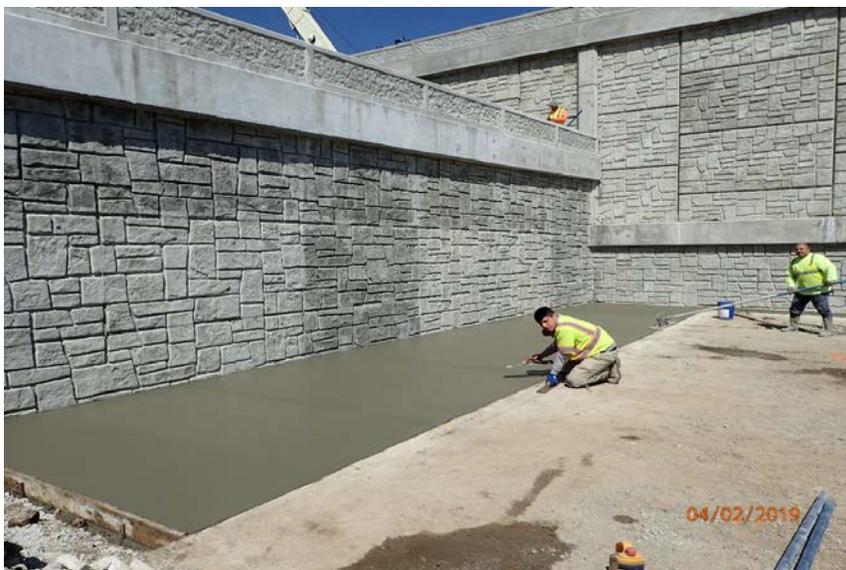

Primco poured the parking lot at Wall 4.



3D fine graded the east end.

# PROJECT PHOTOS



Primco poured the paved side ditch.



Primco poured the sloped wall.




Primco poured the parking lot on the south end of Wall 4.



Primco sandblasted the bridge deck.


# PROJECT PHOTOS

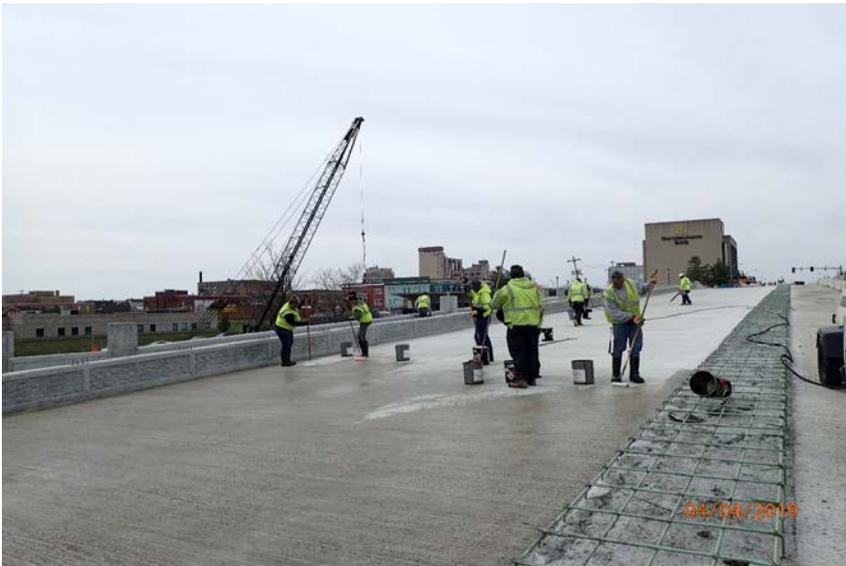

Primco sealed the bridge deck.



Primco placed sealant in the bolt cavities.

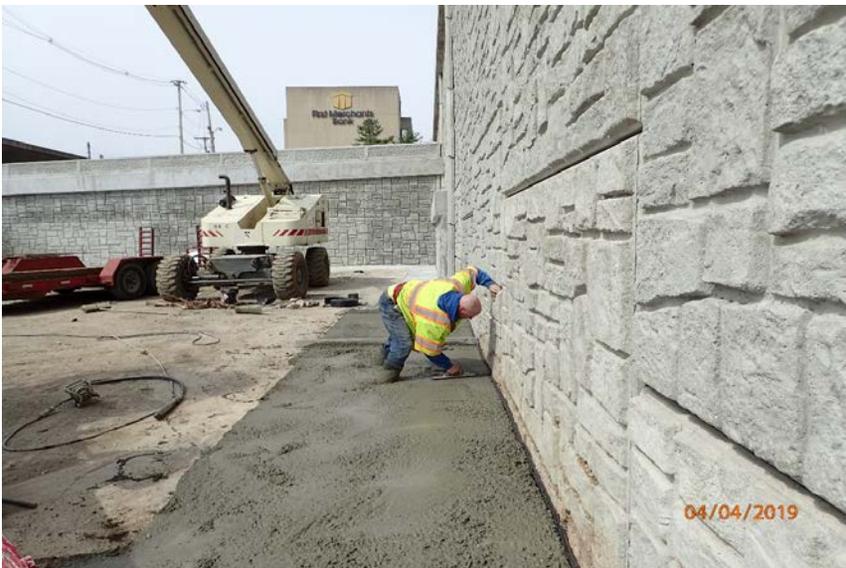

Primco poured the parking lot at Wall 2.



Primco rubbed the bridge deck railing.
