



# WEEKLY REPORT OF CONSTRUCTION ACTIVITIES

**Project Name:** Madison Co. Bridge 502  
**For Week Ending:** 9/2/2017  
**Non-Workable Days to Date:** 4  
**Date of Notice to Proceed:** 4/28/2017  
**Contractor:** Primco, Inc.  
**Owner:** Madison County

**Report No.:** 12  
**Calendar Completion Date:** 8/5/2019  
**This Report:** 0 **Total to Date:** 4  
**Contract Amount:** \$ 13,481,784.02  
**Incurred To Date:** \$ 1,643,913.87  
**Designer:** Beam, Longest, and Neff, LLC

**Contract Number:** B-36317  
**Project Number:** 1297202  
**Structure Number:** 502  
**Balance Remaining:** \$ 11,837,870.15  
**Project Complete Percent:** 12%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 27	No work on site.	Water Main Relocation	Sunday	0/0	No
Mon 28	Primco placed the moment slab stone at Wall 7. 3D excavated for the Wall 7 subgrade treatment. S&S pulled the rock ream.	Water Main Relocation	Able to work on the controlling operation	12/12	Yes
Tues 29	S&S finished the 36in ream. Primco formed the moment slab at Wall 7. 3D hauled off existing concrete structures.	Water Main Relocation	Able to work on the controlling operation	12/12	Yes
Wed 30	S&S started to pull the water main pipe but broke a rod. Primco installed the moment slab reinforcing at Wall 7. 3D undercut the Wall 7 drive.	Water Main Relocation	Able to work on the controlling operation	12/12	Yes
Thurs 31	S&S pulled the water main pipe under the White River. Primco poured the moment slab at Wall 7.	Water Main Relocation	Able to work on the controlling operation	12/12	Yes
Fri 1	S&S placed the electrofusion coupler at the west tee. Primco wrecked forms at Wall 7.	Water Main Relocation	Able to work on the controlling operation	12/12	Yes
Sat 2	No work on site.	Water Main Relocation	Saturday	0/0	No

Distribution:

- Original to Owner
- cc: Project Engineer
- cc: District File
- cc: Contractor

CONTRACTOR ACCEPTANCE

\_\_\_\_\_  
Primco, Inc.

**REMARKS / PROJECTED WORK**

S&S will install the east end electrofusion coupler on Tuesday. 3D will start on the open trench water main work on Tuesday. Culy will start the taps next week. Primo will form and pour the jail approach at Wall 7.

Prepared by:

*Brian Rodgers*

\_\_\_\_\_  
Project Engineer

Approved \_\_\_\_\_, 2017

\_\_\_\_\_  
Madison County

# PROJECT PHOTOS



S&S installed the rock reamer.



Primco formed the moment slab at Wall 7.



S&S fused the last section of water main pipe.



Primco placed reinforcing in the moment slab at Wall 7.

# PROJECT PHOTOS




Primco poured the moment slab at wall 7.



S&S pulled the water main pipe under the river.



S&S finished pulling the water main pipe.

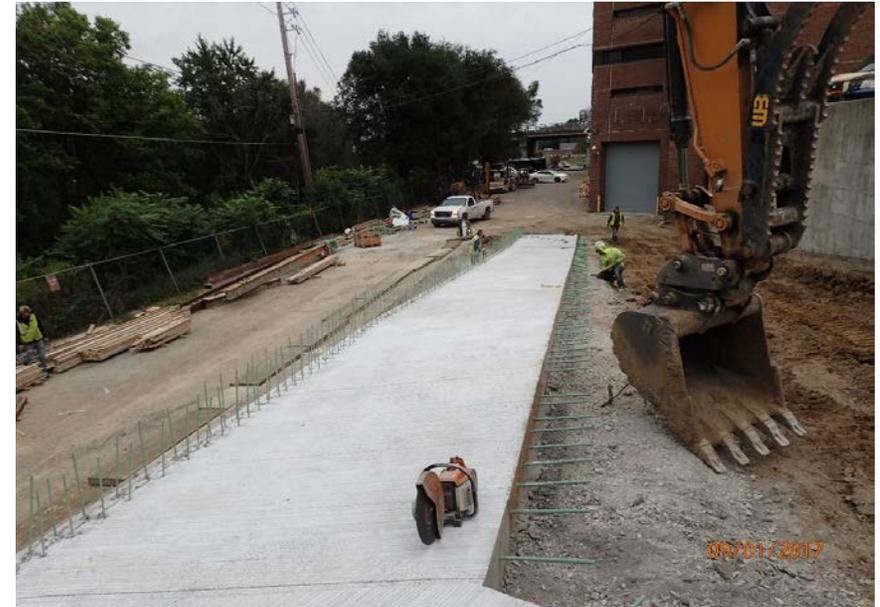

Primco wrecked the moment slab forms.

# PROJECT PHOTOS



3D placed undercut stone and subgrade treatment stone.



S&S removed a section of pipe for the electrofusion coupler.



S&S placed the electrofusion coupler.



S&S placed the electrofusion coupler.
