



WEEKLY REPORT OF CONSTRUCTION ACTIVITIES

Project Name: Madison Co. Bridge 502
For Week Ending: 9/16/2017
Time Elapsed: 14%
Date of Notice to Proceed: 4/28/2017
Contractor: Primco, Inc.
Owner: Madison County

Report No.: 14
Calendar Completion Date: 8/5/2019
Substantial Competition Date: 6/5/2019
Contract Amount: \$ 13,481,784.02
Incurred To Date: \$ 1,662,808.96
Designer: Beam, Longest, and Neff, LLC

Contract Number: B-36317
Project Number: 1297202
Structure Number: 502
Balance Remaining: \$ 11,818,975.06
Project Complete Percent: 12%

| Day and Date | Work in Progress | Current Controlling Operations | Reasons for Reporting As a Work Day or Non-Work Day | Fraction of Day Workable | Work Days Charged |
|--------------|---|--------------------------------|---|--------------------------|-------------------|
| Sun 10 | No work on site. | Water Main Relocation | Sunday | 0/0 | No |
| Mon 11 | Primco formed the jail approach. 3D installed 12in water main. | Water Main Relocation | Able to work on the controlling operation | 10/10 | Yes |
| Tues 12 | Primco poured a section of jail approach. 3D installed 12in water main and excavated for connection 3. | Water Main Relocation | Able to work on the controlling operation | 10/10 | Yes |
| Wed 13 | Primco formed the jail approach. 3D excavated at connection 3 and prepped for the tap. Culy visited the site to review the tap location. | Water Main Relocation | Able to work on the controlling operation | 10/10 | Yes |
| Thurs 14 | Primco poured a section of the jail approach and added backfill in front of Wall 7. 3D installed 24in pipe towards connection 3. C-Tech measured Wall 7 for handrail. | Water Main Relocation | Able to work on the controlling operation | 8/8 | Yes |
| Fri 15 | 3D installed the flushing tap on the 24in main and plugged an abandoned sewer pipe. Primco formed the jail approach and rubbed the PF-1 wall. INDOT red flagged 3D's rental lease with S&S. | Water Main Relocation | Able to work on the controlling operation | 8/8 | Yes |
| Sat 16 | No work on site. | Water Main Relocation | Saturday | 0/0 | No |

Distribution:
 Original to Owner
 cc: Project Engineer
 cc: District File
 cc: Contractor

CONTRACTOR ACCEPTANCE

Primco, Inc.

REMARKS / PROJECTED WORK

Primco will continue pouring the jail approach next week. 3D will continue installing 12in and 24in water main. The taps are expected to be completed next week. Culy is not allowed to perform the taps until INDOT further investigates their rental lease agreement with 3D.

Prepared by:


Brian Rodgers

Project Engineer

Approved _____, 2017

Madison County

PROJECT PHOTOS

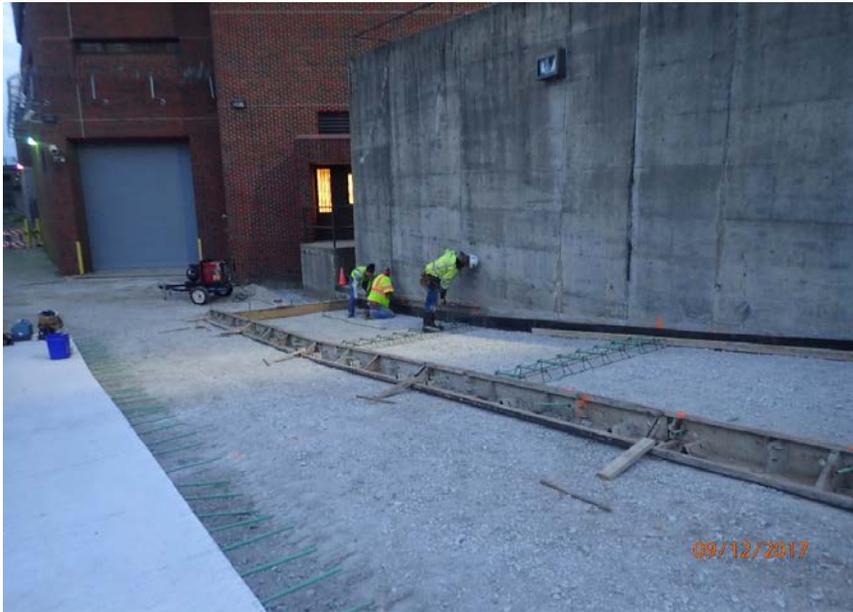

Primco formed the jail approach.



Primco poured the jail approach.



3D excavated the water main at connection 3.



Primco poured the jail approach.

PROJECT PHOTOS



Primco poured the jail approach.



3D installed the 24in water main.



Primco rubbed the PF-1 rail.



Primco installed the 2in flush tap.
