



# WEEKLY REPORT OF CONSTRUCTION ACTIVITIES

**Project Name:** Madison Co. Bridge 502  
**For Week Ending:** 9/30/2017  
**Time Elapsed:** 16%  
**Date of Notice to Proceed:** 4/28/2017  
**Contractor:** Primco, Inc.  
**Owner:** Madison County

**Report No.:** 16  
**Calendar Completion Date:** 8/5/2019  
**Substantial Competition Date:** 6/5/2019  
**Contract Amount:** \$ 13,481,784.02  
**Incurred To Date:** \$ 1,685,894.03  
**Designer:** Beam, Longest, and Neff, LLC

**Contract Number:** B-36317  
**Project Number:** 1297202  
**Structure Number:** 502  
**Balance Remaining:** \$ 11,795,889.99  
**Project Complete Percent:** 13%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 24	No work on site.	Water Main Relocation	Able to work on the controlling operation	8/8	Yes
Mon 25	Primco completed pouring the concrete jail approach at Wall 7.	Water Main Relocation	Able to work on the controlling operation	8/8	Yes
Tues 26	Primco wrecked forms and cleaned up the site.	Water Main Relocation	Able to work on the controlling operation	8/8	Yes
Wed 27	Miller Pipeline started the gas service relocation at the jail. AML&P removed the lights from the bridge. Culy was approved for work on the contract.	Water Main Relocation	Able to work on the controlling operation	8/8	Yes
Thurs 28	3D prepped the water main holes for the taps. Culy placed tapping sleeves at connection 2 and 3. E&B paved the jail lot at Wall 7.	Water Main Relocation	Able to work on the controlling operation	8/8	Yes
Fri 29	3D poured a kicker and valve pad at connection 3. Culy air tested connection 2 and removed the sleeve due to the failed air test. AML&P finished removing the poles from the bridge.	Water Main Relocation	Able to work on the controlling operation	8/8	Yes
Sat 30	No work on site.	Water Main Relocation	Able to work on the controlling operation	8/8	Yes

Distribution:

- Original to Owner
- cc: Project Engineer
- cc: District File
- cc: Contractor

CONTRACTOR ACCEPTANCE

\_\_\_\_\_  
Primco, Inc.

**REMARKS / PROJECTED WORK**

Culy will tap connection 3 on Monday. Connection 2 did not pass an air test due to the roughness and/or shape of the asbestos concrete water main. Culy will be submitting a price for a MJ tapping sleeve. Primco will not be on site until the causeway permit is approved.

Prepared by:


*Brian Rodgers*

\_\_\_\_\_  
Project Engineer

Approved \_\_\_\_\_, 2017

\_\_\_\_\_  
Madison County

# PROJECT PHOTOS

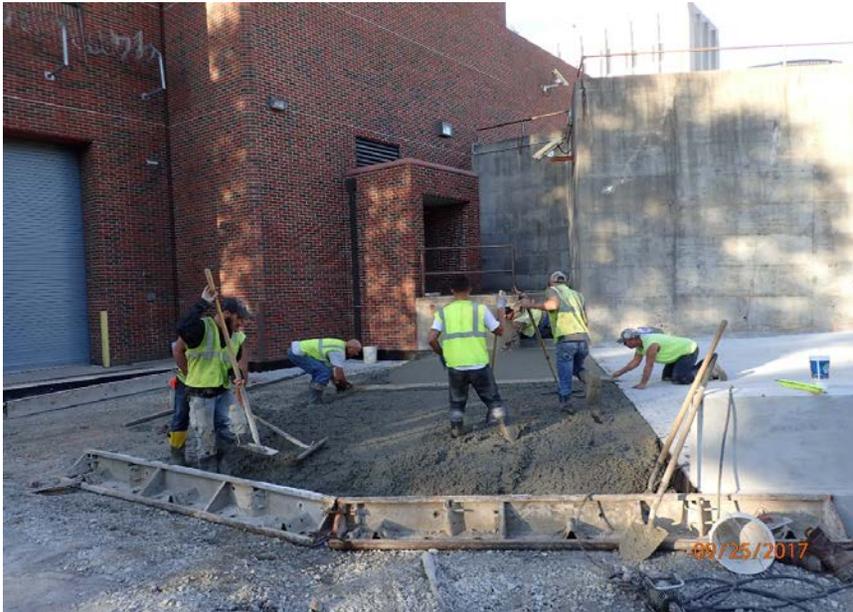

Primco poured a section of jail drive.



Primco poured a section of jail drive.



Miller Pipeline bored the gas service line behind the jail.



Culy installed the tapping sleeve at Connection 3.

# PROJECT PHOTOS



E&B paved the jail lot at Wall 7.



E&B patched Central Ave at the jail approach.



AML&P removed the lights from the bridge.



Culy pressure tested Connection 2.
