

WEEKLY REPORT OF CONSTRUCTION ACTIVITIES



Project Name: Madison Co. Bridge 502
For Week Ending: 12/9/2017
Time Elapsed: 26%
Date of Notice to Proceed: 4/28/2017
Contractor: Primco, Inc.
Owner: Madison County

Report No.: 26
Calendar Completion Date: 8/5/2019
Substantial Competition Date: 6/5/2019
Contract Amount: \$ 13,481,784.02
Incurred To Date: \$ 2,614,134.28
Designer: Beam, Longest, and Neff, LLC

Contract Number: B-36317
Project Number: 1297202
Structure Number: 502
Balance Remaining: \$ 10,867,649.74
Project Complete Percent: 19%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 3	No work on site.	Temp Bridge	Able to work on the controlling operation	8/8	Yes
Mon 4	Primco placed the mudwall on the temp bridge, demoed span 3/4, and pre-tied footing reinf. 3D placed stone in the Work One Lot.	Temp Bridge	Able to work on the controlling operation	8/8	Yes
Tues 5	Primco demoed the existing structure, placed crane mats on the temp bridge, and pre-tied the footing reinf.	Temp Bridge	Able to work on the controlling operation	8/8	Yes
Wed 6	Primco excavated for Wall 2, demoed the existing structure, and moved in the 110t crane. SJ Ludlow submitted the vibration monitoring plan.	Temp Bridge	Able to work on the controlling operation	8/8	Yes
Thurs 7	Primco placed B-borrow at Wall 2, demoed the existing structure, and placed the riprap causeway under span 6 for the demo. 3D saw cut the jail lot.	Temp Bridge	Able to work on the controlling operation	8/8	Yes
Fri 8	Primco drove the test pile at bent 1, placed riprap for the temp bridge, pre tied the footing reinf, and sealed the D1 joints at Wall 7. SJ Ludlow performed the PDA and vibration monitoring.	Temp Bridge	Able to work on the controlling operation	8/8	Yes
Sat 9	No work on site.	Temp Bridge	Able to work on the controlling operation	8/8	Yes

Distribution:

- Original to Owner
- cc: Project Engineer
- cc: District File
- cc: Contractor

CONTRACTOR ACCEPTANCE

Primco, Inc.

REMARKS / PROJECTED WORK

Primco will restrike the test pile at bent 1 on Monday. The PDA test for Pier 2 is scheduled for Wednesday. Primco will start removing the spans over the White River next week.

Prepared by:

Brian Rodgers

Project Engineer

Approved _____, 2017

Madison County

PROJECT PHOTOS




Primco demolished the north structure.



Primco cut up the existing beams.



Primco pre tied the footing and column reinforcing.

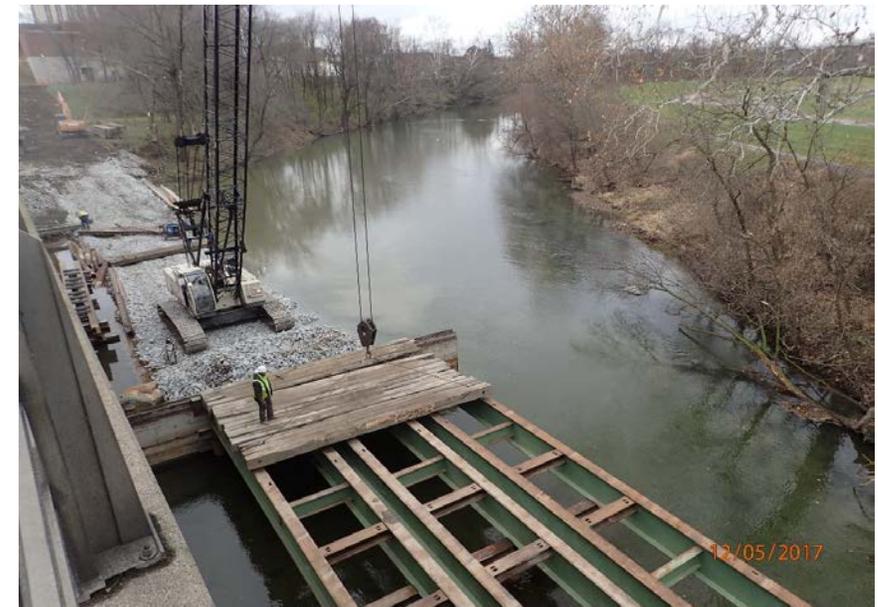

Primco set crane mats on the temp bridge.

PROJECT PHOTOS




3D saw cut the jail parking lot.



Primco placed riprap under Span 6 for the demo.



Primco removed the existing footing.

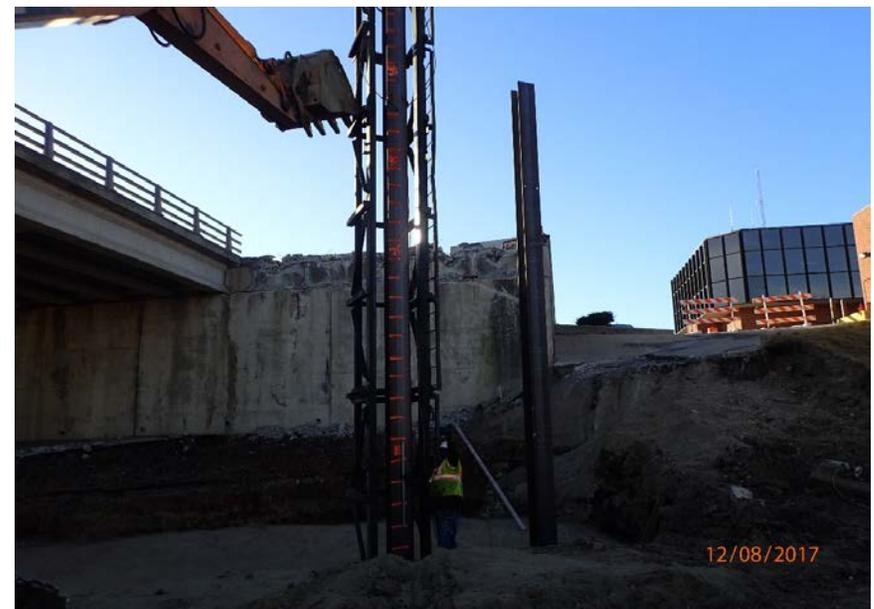

Primco drove the test pile at bent 1.
