



WEEKLY REPORT OF CONSTRUCTION ACTIVITIES

Project Name: Madison Co. Bridge 502
For Week Ending: 1/13/2018
Time Elapsed: 31%
Date of Notice to Proceed: 4/28/2017
Contractor: Primco, Inc.
Owner: Madison County

Report No.: 31
Calendar Completion Date: 8/5/2019
Substantial Competition Date: 6/5/2019
Contract Amount: \$ 13,481,784.02
Incurred To Date: \$ 2,966,860.11
Designer: Beam, Longest, and Neff, LLC

Contract Number: B-36317
Project Number: 1297202
Structure Number: 502
Balance Remaining: \$ 10,514,923.91
Project Complete Percent: 22%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 7	No work on site.	Substructure	Able to work on the controlling operation	8/8	Yes
Mon 8	Primco formed the Pier 2 columns, started the cofferdam at Pier 4, and continued the bridge demo.	Substructure	Able to work on the controlling operation	8/8	Yes
Tues 9	Primco poured the Pier 2 columns, installed the cofferdam at Pier 4, and continued the bridge demo.	Substructure	Able to work on the controlling operation	8/8	Yes
Wed 10	Primco removed the Pier 2 column forms, placed resteel for the Pier 3 columns, installed the cofferdam at Pier 4, and continued the bridge demo.	Substructure	Able to work on the controlling operation	8/8	Yes
Thurs 11	Primco poured the Pier 3 columns, installed the cofferdam at Pier 4, and pre-tied column resteel.	Substructure	Able to work on the controlling operation	8/8	Yes
Fri 12	Primco removed the Pier 3 column forms, completed the cofferdam at Pier 4, and continued the bridge demo.	Substructure	Able to work on the controlling operation	6/6	Yes
Sat 13	No work on site.	Substructure	Able to work on the controlling operation	8/8	Yes

Distribution:
 Original to Owner
 cc: Project Engineer
 cc: District File
 cc: Contractor

REMARKS / PROJECTED WORK

Primco will excavate the Pier 4 cofferdam on Monday. The PDA testing for Pier 4 is scheduled for Monday.

Prepared by: Brian Rodgers
 Project Engineer

Approved _____, 2018

_____ Madison County

CONTRACTOR ACCEPTANCE

Primco, Inc.

PROJECT PHOTOS




Primco prepped the resteel for the forms.



Primco placed the column forms at Pier 2.



Primco started the cofferdam sheeting at Pier 4.

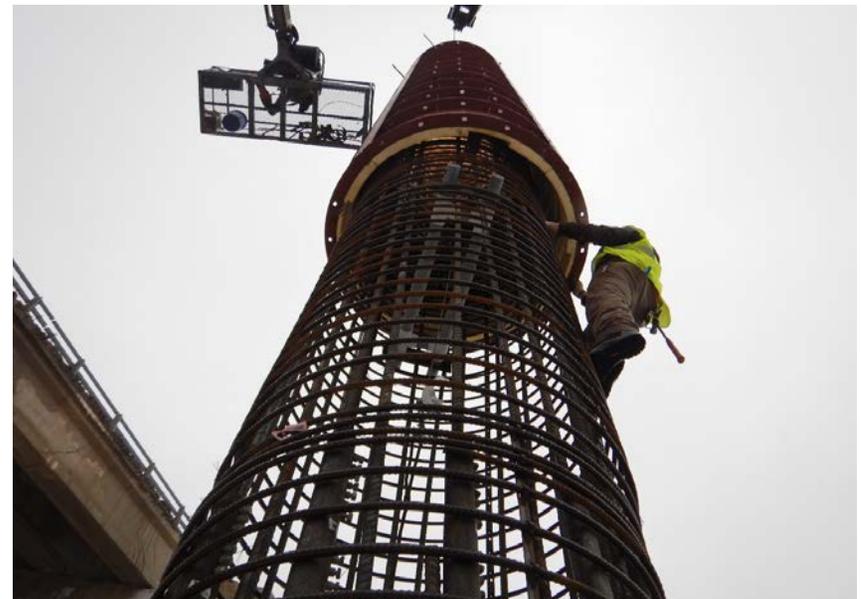

Primco placed the column forms.

PROJECT PHOTOS



Primco poured the Pier 2 columns.



Primco removed the Pier 2 column forms.



Primco drove sheeting for the Pier 4 cofferdam.



Primco demoed the last span.
