



WEEKLY REPORT OF CONSTRUCTION ACTIVITIES

Project Name: Madison Co. Bridge 502
For Week Ending: 2/17/2018
Time Elapsed: 36%
Date of Notice to Proceed: 4/28/2017
Contractor: Primco, Inc.
Owner: Madison County

Report No.: 36
Calendar Completion Date: 8/5/2019
Substantial Competition Date: 6/5/2019
Contract Amount: \$ 13,481,784.02
Incurred To Date: \$ 3,431,748.38
Designer: Beam, Longest, and Neff, LLC

Contract Number: B-36317
Project Number: 1297202
Structure Number: 502
Balance Remaining: \$ 10,050,035.64
Project Complete Percent: 25%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 11	No work on site.	Substructure	Able to work on the controlling operation	8/8	Yes
Mon 12	Primco placed the resteel for the Pier 5 columns and formed the Pier 4 cap.	Substructure	Able to work on the controlling operation	8/8	Yes
Tues 13	Primco poured the Pier 3 columns, formed the Pier 4 cap, and wrecked the Bent 7 forms.	Substructure	Able to work on the controlling operation	8/8	Yes
Wed 14	Primco poured the Pier 4 cap and wrecked the Pier 5 column forms.	Substructure	Able to work on the controlling operation	8/8	Yes
Thurs 15	Primco pre-tied the Pier 5 cap resteel, removed the Pier 4 cap face forms, and placed sheeting at Pier 6.	Substructure	Able to work on the controlling operation	8/8	Yes
Fri 16	Primco placed sheeting for the Pier 6 cofferdam, formed the leveling pad at Wall 2, and pre-tied the Pier 5 cap resteel. Roadsafe fixed the damaged barricade.	Substructure	Able to work on the controlling operation	8/8	Yes
Sat 17	No work on site.	Substructure	Able to work on the controlling operation	8/8	Yes

Distribution:

- Original to Owner
- cc: Project Engineer
- cc: District File
- cc: Contractor

CONTRACTOR ACCEPTANCE

Primco, Inc.

REMARKS / PROJECTED WORK

Primco will pour a section of the Wall 2 leveling pad on Tuesday. Primco will continue driving the sheeting for the Pier 6 cofferdam next week. Crews will start forming the Pier 5 cap.

Prepared by:

Brian Rodgers

Project Engineer

Approved _____, 2018

Madison County

PROJECT PHOTOS



Primco placed the resteel for the Pier 5 columns.



Primco formed the Pier 4 cap.



Primco pre-tied the Pier 5 cap.




Project photo from the Blue Bridge.

PROJECT PHOTOS



Primco poured the Pier 5 columns.

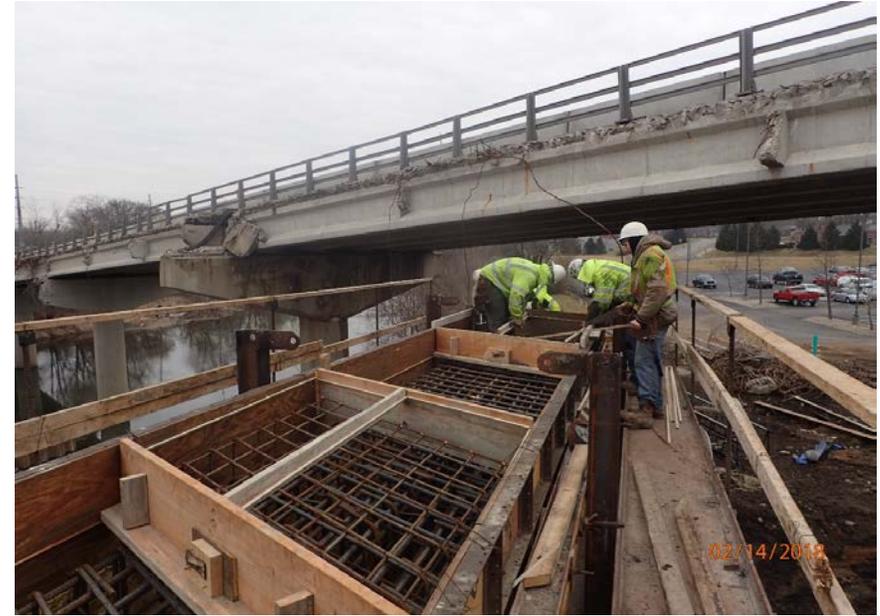

Primco formed the Pier 4 cap.



Primco wrecked the Pier 5 column forms.



Primco drove sheeting for the Pier 6 cofferdam.
