



# WEEKLY REPORT OF CONSTRUCTION ACTIVITIES

**Project Name:** Madison Co. Bridge 502  
**For Week Ending:** 3/3/2018  
**Time Elapsed:** 38%  
**Date of Notice to Proceed:** 4/28/2017  
**Contractor:** Primco, Inc.  
**Owner:** Madison County

**Report No.:** 38  
**Calendar Completion Date:** 8/5/2019  
**Substantial Competition Date:** 6/5/2019  
**Contract Amount:** \$ 13,481,784.02  
**Incurred To Date:** \$ 4,587,564.02  
**Designer:** Beam, Longest, and Neff, LLC

**Contract Number:** B-36317  
**Project Number:** 1297202  
**Structure Number:** 502  
**Balance Remaining:** \$ 8,894,220.00  
**Project Complete Percent:** 34%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 25	No work on site.	Substructure	Able to work on the controlling operation	8/8	Yes
Mon 26	Primco constructed Wall 2 and 6. The temporary floodwall at Bent 7 was installed.	Substructure	Able to work on the controlling operation	8/8	Yes
Tues 27	Primco constructed Wall 2 and 6, drove sheeting for the north I-wall, and excavated the Pier 6 cofferdam.	Substructure	Able to work on the controlling operation	8/8	Yes
Wed 28	Primco drove all the Phase 1 piles at Pier 6 and formed the north I-wall at Bent 7.	Substructure	Able to work on the controlling operation	8/8	Yes
Thurs 1	Primco constructed Wall 2 and 6. Crews formed the north I-wall at Bent 7.	Substructure	Able to work on the controlling operation	8/8	Yes
Fri 2	Primco poured the north I-wall at Bent 7, removed the falsework at Pier 5, and constructed Walls 2 and 6.	Substructure	River in flood stage. Water over the Pier 6 cofferdam.	0/0	No
Sat 3	No work on site.	Substructure	River in flood stage. Water over the Pier 6 cofferdam.	0/0	No

Distribution:

- Original to Owner
- cc: Project Engineer
- cc: District File
- cc: Contractor

CONTRACTOR ACCEPTANCE

\_\_\_\_\_  
Primco, Inc.

**REMARKS / PROJECTED WORK**

Primco will pour the Pier 6 footings and columns next week. Crews will continue constructing Wall 2 and 6. 3D will add and repair the erosion control items on Monday.

Prepared by:

*Brian Rodgers*

\_\_\_\_\_  
Project Engineer

Approved \_\_\_\_\_, 2018

\_\_\_\_\_  
Madison County

# PROJECT PHOTOS



Primco drove sheeting for the north I-wall at Bent 7.



Primco constructed Wall 2.



Primco constructed Wall 2.



Primco pre-tied the Pier 6 cap resteel.

# PROJECT PHOTOS




Primco constructed Wall 2.



Primco drove piling at Pier 6.



Primco formed the north I-wall at Bent 7.

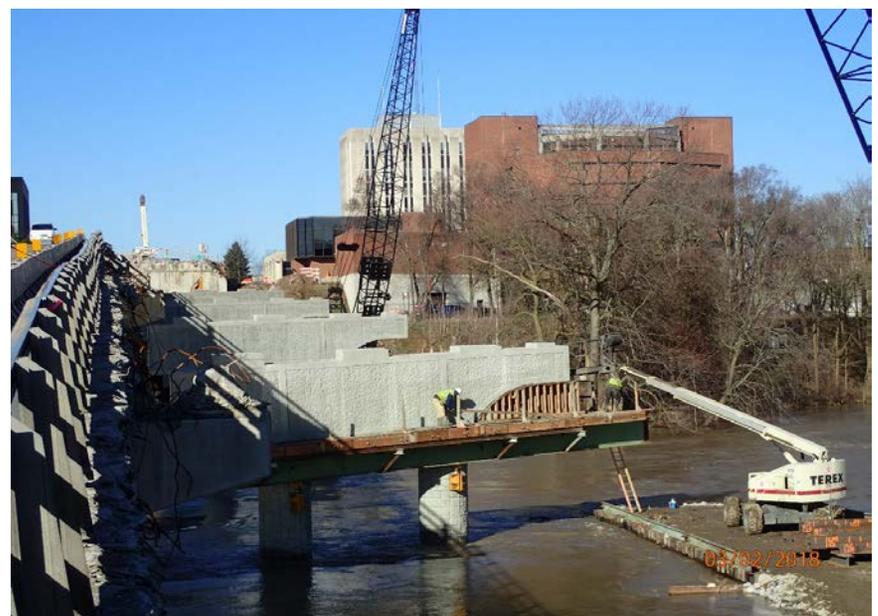

Primco wrecked the Pier 5 falsework.
