

WEEKLY REPORT OF CONSTRUCTION ACTIVITIES



Project Name: Madison Co. Bridge 502
For Week Ending: 3/10/2018
Time Elapsed: 38%
Date of Notice to Proceed: 4/28/2017
Contractor: Primco, Inc.
Owner: Madison County

Report No.: 39
Calendar Completion Date: 8/5/2019
Substantial Competition Date: 6/5/2019
Contract Amount: \$ 13,481,784.02
Incurred To Date: \$ 4,738,188.38
Designer: Beam, Longest, and Neff, LLC

Contract Number: B-36317
Project Number: 1297202
Structure Number: 502
Balance Remaining: \$ 8,743,595.64
Project Complete Percent: 35%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 4	No work on site.	Substructure	Able to work on the controlling operation	8/8	Yes
Mon 5	Primco constructed Wall 2/6 and poured the Pier 6 footings.	Substructure	Able to work on the controlling operation	8/8	Yes
Tues 6	Primco wrecked the levee forms, removed the existing east bent, graded for the block mattress, and constructed Wall 2/6.	Substructure	Able to work on the controlling operation	8/8	Yes
Wed 7	Primco constructed Wall 2/6 and poured the Pier 6 columns.	Substructure	Able to work on the controlling operation	8/8	Yes
Thurs 8	Primco constructed Wall 2/6 and pulled the cofferdam sheeting at Pier 6.	Substructure	Able to work on the controlling operation	8/8	Yes
Fri 9	Primco finished pulling the cofferdam sheeting at Pier 6, graded the east bank, added filter log to the east bank, and constructed Wall 2/6.	Substructure	Able to work on the controlling operation	8/8	Yes
Sat 10	No work on site.	Substructure	Able to work on the controlling operation	8/8	Yes

Distribution:

- Original to Owner
- cc: Project Engineer
- cc: District File
- cc: Contractor

CONTRACTOR ACCEPTANCE

Primco, Inc.

REMARKS / PROJECTED WORK

Primco will pour the Pier 6 cap on Tuesday. The fill at Wall 2 is approximately 1ft below the bottom of Bent 1. Primco will continue to construct Wall 2 and then start forming Bent 1. The first span of beams are scheduled for March 21st.

Prepared by:

Brian Rodgers

Project Engineer


Approved _____, 2018

Madison County

PROJECT PHOTOS




Primco constructed Wall 2.

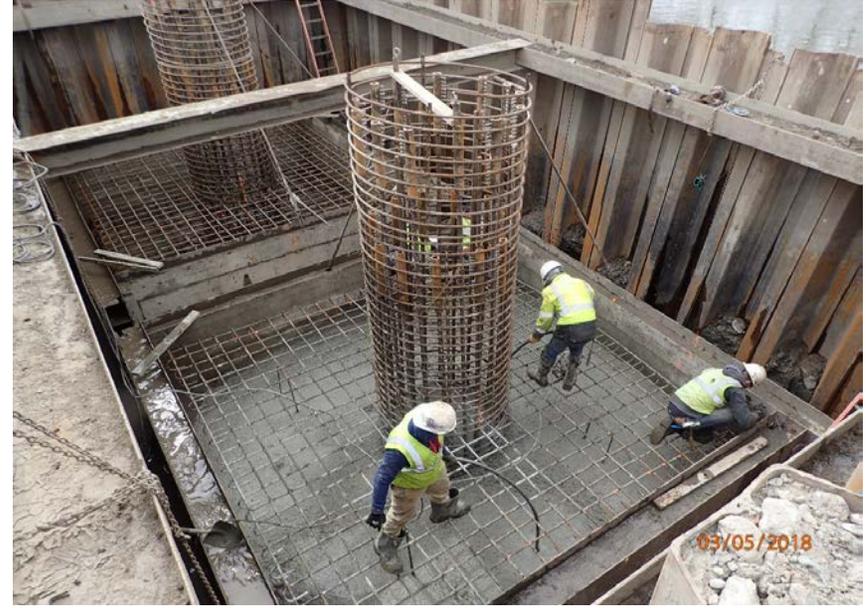

Primco poured the Pier 6 footings with Class C concrete.



Primco constructed Wall 2.

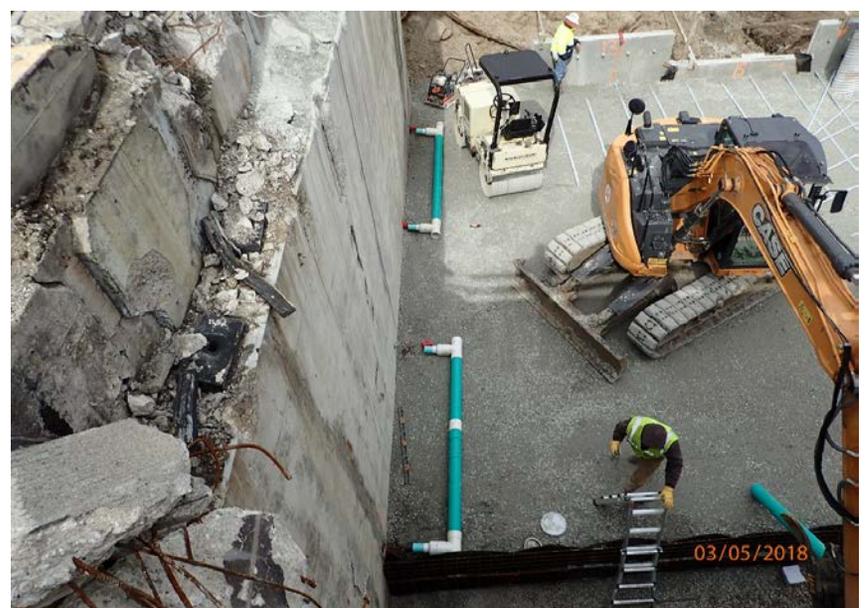


3D extended the weep drains behind Wall 2.

PROJECT PHOTOS



3D cleaned up and touched up the filter berm.

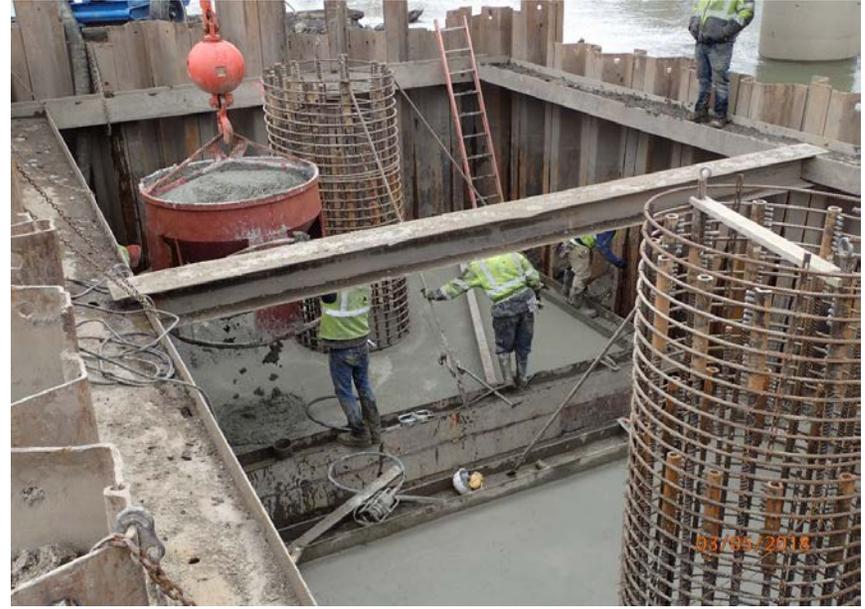

Primco poured the Pier 6 footings.



Primco wrecked the Pier 6 columns.



Primco constructed Wall 2.
