



# WEEKLY REPORT OF CONSTRUCTION ACTIVITIES

**Project Name:** Madison Co. Bridge 502  
**For Week Ending:** 3/17/2018  
**Time Elapsed:** 39%  
**Date of Notice to Proceed:** 4/28/2017  
**Contractor:** Primco, Inc.  
**Owner:** Madison County

**Report No.:** 40  
**Calendar Completion Date:** 8/5/2019  
**Substantial Competition Date:** 6/5/2019  
**Contract Amount:** \$ 13,481,784.02  
**Incurred To Date:** \$ 4,843,901.85  
**Designer:** Beam, Longest, and Neff, LLC

**Contract Number:** B-36317  
**Project Number:** 1297202  
**Structure Number:** 502  
**Balance Remaining:** \$ 8,637,882.17  
**Project Complete Percent:** 36%

| Day and Date | Work in Progress   | Current Controlling Operations | Reasons for Reporting As a Work Day or Non-Work Day | Fraction of Day Workable | Work Days Charged |
|--------------|--|--------------------------------|---|--------------------------|-------------------|
| Sun<br>11    | No work on site.   | Substructure                   | Able to work on the controlling operation           | 8/8                      | Yes               |
| Mon<br>12    | Primco formed the Pier 6 cap, backfilled Wall 2, placed resteel for Bent 1, and removed portions of the existing retaining wall.                 | Substructure                   | Able to work on the controlling operation           | 8/8                      | Yes               |
| Tues<br>13   | Primco poured the Pier 6 cap, placed resteel at Bent 1, and prepped for the articulating concrete mattress at Bent 7.                            | Substructure                   | Able to work on the controlling operation           | 8/8                      | Yes               |
| Wed<br>14    | Primco placed the articulating concrete mattress at Bent 7 and formed Bent 1. Slussers laid out the trees at the off-site planting area.         | Substructure                   | Able to work on the controlling operation           | 8/8                      | Yes               |
| Thurs<br>15  | Primco formed Bent 1, removed portions of the existing wall, and placed the articulating concrete mattress at Bent 7. Slussers planted 70 trees. | Substructure                   | Able to work on the controlling operation           | 8/8                      | Yes               |
| Fri<br>16    | Primco poured Bent 1, grouted the articulating concrete mattress seams, and added riprap to the causeway. Michiana poured a light foundation.    | Substructure                   | Able to work on the controlling operation           | 8/8                      | Yes               |
| Sat<br>17    | No work on site.   | Substructure                   | Able to work on the controlling operation           | 8/8                      | Yes               |

Distribution:

- Original to Owner
- cc: Project Engineer
- cc: District File
- cc: Contractor

CONTRACTOR ACCEPTANCE

\_\_\_\_\_  
Primco, Inc.

**REMARKS / PROJECTED WORK**

Primco will set beams on Wednesday, Thursday, and Friday. The eastbound lane will be closed from 9:00AM to 4:00PM while the beams are set.

Prepared by:

*Brian Rodgers*

\_\_\_\_\_  
Project Engineer

Approved \_\_\_\_\_, 2018

\_\_\_\_\_  
Madison County

# PROJECT PHOTOS



Primco constructed Wall 2.



Primco formed the Pier 6 cap.



Primco installed the Pier 6 cap reinforcing.



Primco poured the Pier 6 cap.

# PROJECT PHOTOS



Primco tied the Bent 1 reinforcing.



Primco removed portions of the existing wall.




Primco placed the articulating concrete mattress at Bent 7.



Slussers planted trees at the off-site planting area.

# PROJECT PHOTOS

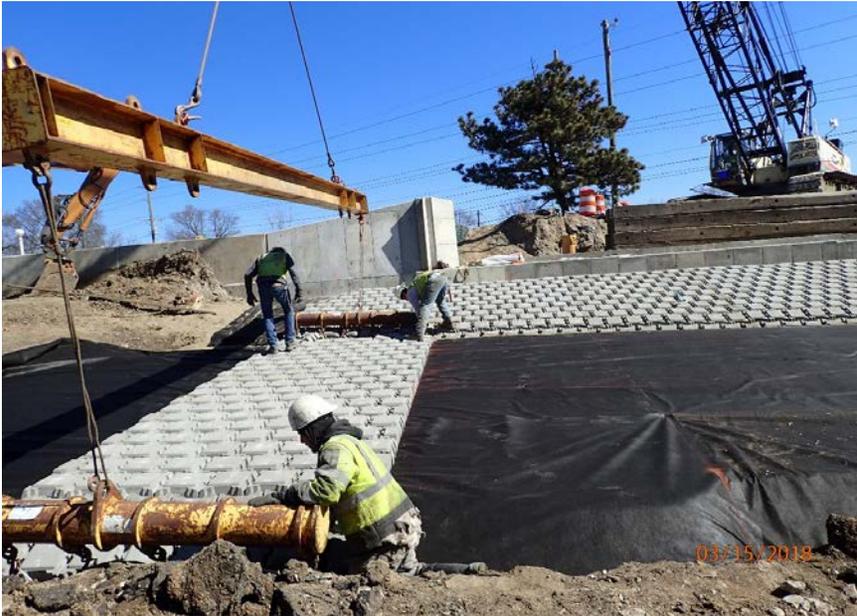

Primco placed the articulated concrete mattress at Bent 7.



Primco grouted the seams and backfilled the mattress.



Primco poured Bent 1.



Michiana installed the light foundation at the end of Wall 3.
