



WEEKLY REPORT OF CONSTRUCTION ACTIVITIES

Project Name: Madison Co. Bridge 502
For Week Ending: 3/24/2018
Time Elapsed: 40%
Date of Notice to Proceed: 4/28/2017
Contractor: Primco, Inc.
Owner: Madison County

Report No.: 41
Calendar Completion Date: 8/5/2019
Substantial Competition Date: 6/5/2019
Contract Amount: \$ 13,481,784.02
Incurred To Date: \$ 5,987,279.46
Designer: Beam, Longest, and Neff, LLC

Contract Number: B-36317
Project Number: 1297202
Structure Number: 502
Balance Remaining: \$ 7,494,504.56
Project Complete Percent: 44%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 18	No work on site.	Substructure	Able to work on the controlling operation	8/8	Yes
Mon 19	Primco wrecked the Pier 6 falsework, constructed Wall 6, and removed the existing retaining wall. Bertsch-Frank laid out the bearing pads.	Substructure	Able to work on the controlling operation	8/8	Yes
Tues 20	Primco installed the bearing assemblies, prepped for beams, and backfilled Wall 2/6.	Superstructure	Able to work on the controlling operation	8/8	Yes
Wed 21	Primco backfilled Wall 2, cleaned up the site, and removed the west approach.	Superstructure	Beam delivery canceled by the State Police due to snow	0/8	No
Thurs 22	Primco set the Span E beams and formed the Wall 2 coping. The eastbound lane was shut down from 9-4.	Superstructure	Able to work on the controlling operation	10/10	Yes
Fri 23	Primco set the Span F beams, poured the Wall 2 coping, and unloaded deck resteel. The eastbound lane was shut down from 9:45-4. Pre-Stress completed the Phase 2 beams.	Superstructure	Able to work on the controlling operation	10/10	Yes
Sat 24	No work on site.	Superstructure	Able to work on the controlling operation	8/8	Yes

Distribution:

- Original to Owner
- cc: Project Engineer
- cc: District File
- cc: Contractor

CONTRACTOR ACCEPTANCE

Primco, Inc.

REMARKS / PROJECTED WORK

Primco will continue setting U-beams on Monday, Tuesday, Wednesday, and Friday. The eastbound lane will be closed from 9AM to 4PM. A progress meeting is scheduled for Wednesday, March 28 at 10:30AM.

Prepared by:

Brian Rodgers

Project Engineer

Approved _____, 2018

Madison County

PROJECT PHOTOS



Primco prepped for the beams



Bertsch-Frank laid out the bearing assemblies.



Primco formed the Wall 2 coping.



Primco removed the west approach.

PROJECT PHOTOS



Primco set the bearing assemblies.



Primco set the Span E beams.



Primco set the Span E beams.



Primco set the Span E beams.

PROJECT PHOTOS



Primco set the Span E beams.



Primco set the Span E beams.



Primco set the Span F beams.



Primco set the Span F beams.

PROJECT PHOTOS




Primco set the Span F beams.



Primco set the Span F beams.



Primco set the Span F beams.

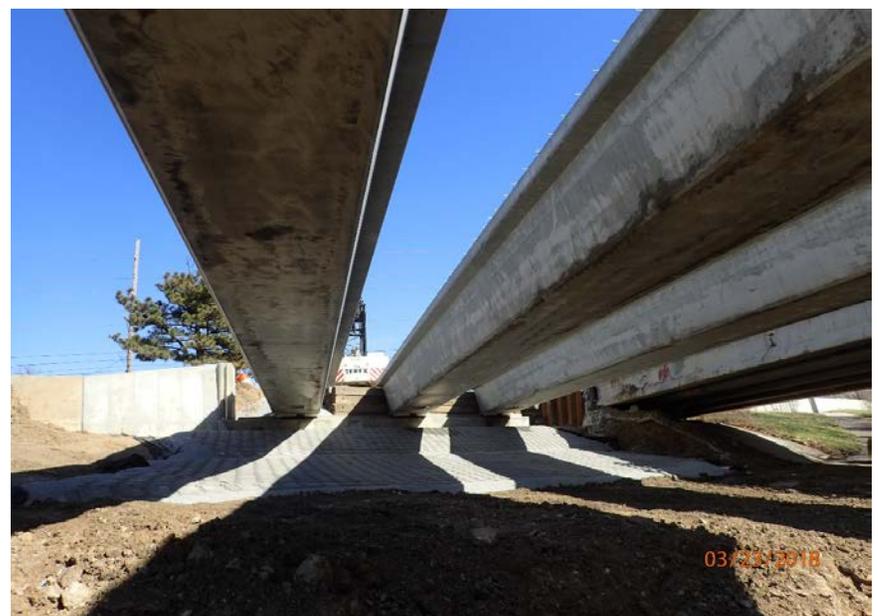

Primco set the Span F beams.
