

# WEEKLY REPORT OF CONSTRUCTION ACTIVITIES



**Project Name:** Madison Co. Bridge 502  
**For Week Ending:** 4/21/2018  
**Time Elapsed:** 44%  
**Date of Notice to Proceed:** 4/28/2017  
**Contractor:** Primco, Inc.  
**Owner:** Madison County

**Report No.:** 45  
**Calendar Completion Date:** 8/5/2019  
**Substantial Competition Date:** 6/5/2019  
**Contract Amount:** \$ 13,481,784.02  
**Incurred To Date:** \$ 6,789,096.38  
**Designer:** Beam, Longest, and Neff, LLC

**Contract Number:** B-36317  
**Project Number:** 1297202  
**Structure Number:** 502  
**Balance Remaining:** \$ 6,692,687.64  
**Project Complete Percent:** 50%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 15	No work on site.	Superstructure	Able to work on the controlling operation	8/8	Yes
Mon 16	Primco installed deck pans and falsework. Bertsch Frank stated the west end. 3D unloaded pipe.	Superstructure	Able to work on the controlling operation	8/8	Yes
Tues 17	Primco finished the deck pans, installed falsework, and formed the diaphragms. 3D excavated the west end road approach.	Superstructure	Able to work on the controlling operation	8/8	yes
Wed 18	Primco formed the diaphragms, placed falsework, and formed the deck. 3D excavated the west end road approach.	Superstructure	Able to work on the controlling operation	8/8	Yes
Thurs 19	Primco tied the diaphragm reinforcing, formed the diaphragms, and formed the deck. 3D excavated the strap zone for Wall 3.	Superstructure	Able to work on the controlling operation	8/8	Yes
Fri 20	Primco formed the deck, tied the diaphragm reinforcing, and placed stone under the Wall 3 leveling pad.	Superstructure	Able to work on the controlling operation	8/8	Yes
Sat 21	Primco placed temp sheeting at the west phase line, formed the diaphragms, and cleaned the deck.	Superstructure	Able to work on the controlling operation	8/8	Yes

Distribution:

- Original to Owner
- cc: Project Engineer
- cc: District File
- cc: Contractor

CONTRACTOR ACCEPTANCE

\_\_\_\_\_  
Primco, Inc.

**REMARKS / PROJECTED WORK**

Harmon will start tying the deck reinforcing on Monday. Primco will continue forming the deck and diaphragms toward the west.

Prepared by:

*Brian Rodgers*

\_\_\_\_\_  
Project Engineer

Approved \_\_\_\_\_, 2018

\_\_\_\_\_  
Madison County

# PROJECT PHOTOS



Primco installed the deck pans.



Primco installed the falsework and railing.



Primco placed foam board at the diaphragms.



Primco formed the phase line.


# PROJECT PHOTOS



Primco formed the deck.



3D excavated for Wall 3.

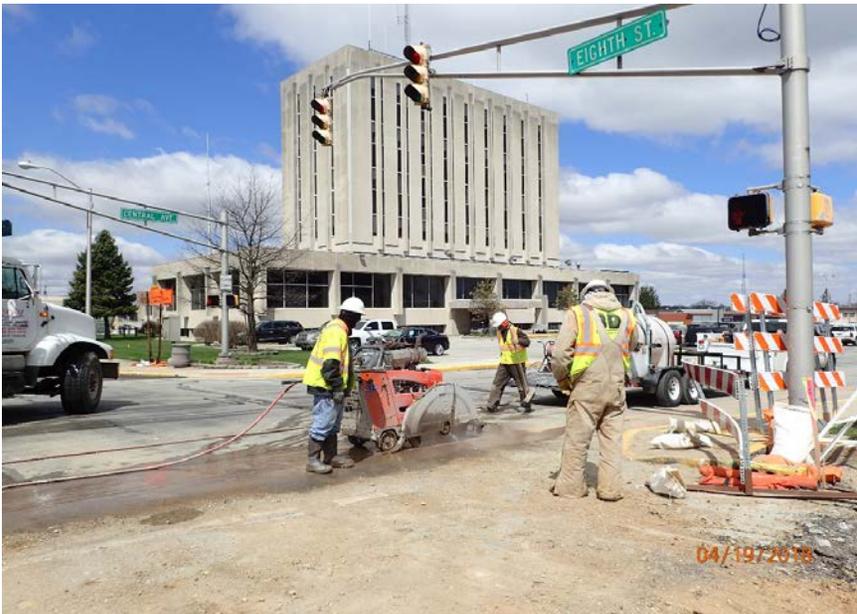

3D saw cut the west end.



Primco installed the coping falsework.

# PROJECT PHOTOS



Primco formed the deck.



Primco formed the deck.



3D excavated the west end road approach.



Primco formed the phase line.

# PROJECT PHOTOS



Primco placed stone under the leveling pad at Wall 3.



Primco placed form ties at the pier diaphragms.



Primco placed temp sheeting at the west end phaseline.



Primco laid out the top of deck.
