

# WEEKLY REPORT OF CONSTRUCTION ACTIVITIES



**Project Name:** Madison Co. Bridge 502  
**For Week Ending:** 4/28/2018  
**Time Elapsed:** 45%  
**Date of Notice to Proceed:** 4/28/2017  
**Contractor:** Primco, Inc.  
**Owner:** Madison County

**Report No.:** 46  
**Calendar Completion Date:** 8/5/2019  
**Substantial Competition Date:** 6/5/2019  
**Contract Amount:** \$ 13,481,784.02  
**Incurred To Date:** \$ 6,818,584.32  
**Designer:** Beam, Longest, and Neff, LLC

**Contract Number:** B-36317  
**Project Number:** 1297202  
**Structure Number:** 502  
**Balance Remaining:** \$ 6,663,199.70  
**Project Complete Percent:** 51%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 22	No work on site.	Superstructure	Able to work on the controlling operation	8/8	Yes
Mon 23	Primco formed the deck and diaphragms. Harmon laid out the bottom mat. 3D set Str 11 and 13.	Superstructure	Able to work on the controlling operation	7/8	Yes
Tues 24	Primco formed the diaphragms and installed falsework. Harmon tied the bottom mat of Spans 5 and 6.	Superstructure	Able to work on the controlling operation	8/8	Yes
Wed 25	Primco formed the deck and diaphragms. Harmon tied the bottom mat of spans 4-6 and the coping railing reinf. 3D excavated the east roadway.	Superstructure	Able to work on the controlling operation	8/8	Yes
Thurs 26	Primco poured the Bent 1 diaphragm and the Wall 3 leveling pad. Harmon tied the coping railing reinf. 3D excavated the east roadway. Michiana installed conduit.	Superstructure	Able to work on the controlling operation	8/8	Yes
Fri 27	Primco formed the deck and installed tie bars. Harmon tied the top mat of spans 5 and 6. 3D removed the sidewalk on the west end and excavated the roadway on the east end.	Superstructure	Able to work on the controlling operation	8/8	Yes
Sat 28	Primco set Wall 3 panels and formed the deck.	Superstructure	Able to work on the controlling operation	6/6	Yes

Distribution:

- Original to Owner
- cc: Project Engineer
- cc: District File
- cc: Contractor

CONTRACTOR ACCEPTANCE

\_\_\_\_\_  
Primco, Inc.

**REMARKS / PROJECTED WORK**

The east half of the deck will be poured on Friday, May 4th. A pre-pour meeting will be held Wednesday, May 2nd at 10:30AM.

Prepared by:

*Brian Rodgers*

\_\_\_\_\_  
Project Engineer

Approved \_\_\_\_\_, 2018

\_\_\_\_\_  
Madison County

# PROJECT PHOTOS



3D poured the flowline in Str 13.



Primco formed the deck.




Harmon installed the bottom mat reinforcing.



Primco installed the threaded tie bars.

# PROJECT PHOTOS

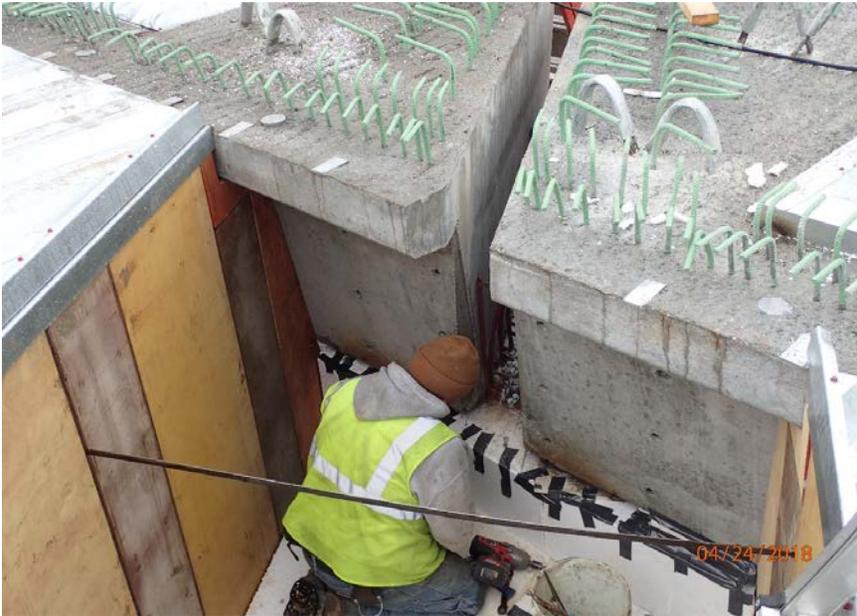

Primco added the strand clamps.



3D saw cut the east end pavement.



Michiana installed the lighting conduit.



3D excavated the east end roadway.

# PROJECT PHOTOS



Harmon tied the top mat reinforcing.



Primco backfilled Wall 2.



Harmon tied the top mat reinforcing.



Primco placed the Wall 3 panels.
