



WEEKLY REPORT OF CONSTRUCTION ACTIVITIES

Project Name: Madison Co. Bridge 502
For Week Ending: 5/12/2018
Time Elapsed: 47%
Date of Notice to Proceed: 4/28/2017
Contractor: Primco, Inc.
Owner: Madison County

Report No.: 48
Calendar Completion Date: 8/5/2019
Substantial Competition Date: 6/5/2019
Contract Amount: \$ 13,481,784.02
Incurred To Date: \$ 7,334,555.45
Designer: Beam, Longest, and Neff, LLC

Contract Number: B-36317
Project Number: 1297202
Structure Number: 502
Balance Remaining: \$ 6,147,228.57
Project Complete Percent: 54%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 6	No work on site.	Superstructure	Able to work on the controlling operation	8/8	Yes
Mon 7	Primco poured the east half of the deck and placed flowfill at Wall 3. 3D excavated for subgrade treatment. Harmon tied reinf steel.	Superstructure	Able to work on the controlling operation	8/8	Yes
Tues 8	Primco flowfilled Wall 3, installed screed rails, and wrecked deck forms. 3D placed subgrade treatment. Michiana placed conduit. Harmon tied reinf steel.	Superstructure	Able to work on the controlling operation	8/8	Yes
Wed 9	Primco prepped for the deck pour. 3D placed subgrade treatment stone for the east approach. Harmon completed the deck reinf.	Superstructure	Able to work on the controlling operation	8/8	Yes
Thurs 10	Primco completed a dry run and prepped for the deck pour. 3D placed subgrade treatment stone on the east approach.	Superstructure	Able to work on the controlling operation	8/8	Yes
Fri 11	Primco poured the west half of the deck.	Superstructure	Able to work on the controlling operation	8/8	Yes
Sat 12	No work on site.	Superstructure	Able to work on the controlling operation	8/8	Yes

Distribution:

- Original to Owner
- cc: Project Engineer
- cc: District File
- cc: Contractor

CONTRACTOR ACCEPTANCE

Primco, Inc.

REMARKS / PROJECTED WORK

Primco will pour the sleeper slabs next week. The approaches will be formed and pour thereafter.

Prepared by:

Brian Rodgers

Project Engineer

Approved _____, 2018

Madison County

PROJECT PHOTOS



Primco poured the deck.



Primco poured the deck.



Primco tined the deck.



Primco poured the deck.


PROJECT PHOTOS




Primco covered the deck.



Primco finished the deck.

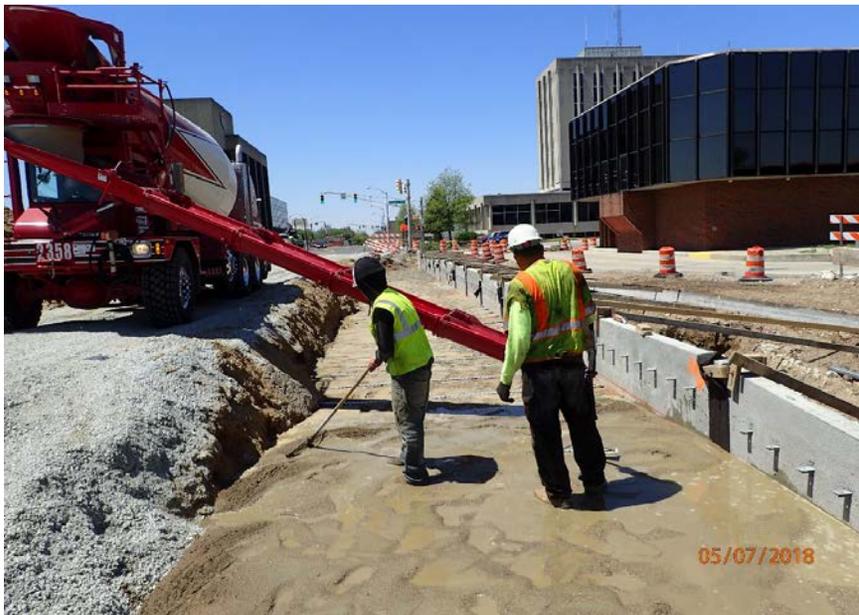

Primco placed flowfill at Wall 3.

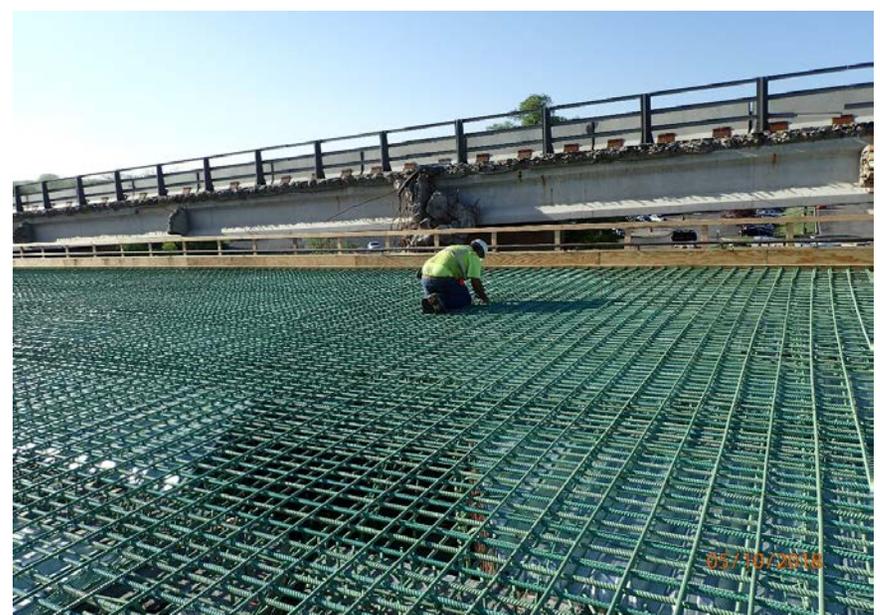

Primco added chairs near the diaphragms.

PROJECT PHOTOS



3D placed subgrade treatment stone on the east road approach.



Primco poured the deck.



Primco filled the diaphragms ahead of the finishing machine.



Primco finished the deck.

PROJECT PHOTOS



Primco probed the locations of the interior railing bars.



Primco poured the deck.



Primco finished the deck.



Primco covered the deck.
