

# WEEKLY REPORT OF CONSTRUCTION ACTIVITIES

**Project Name:** Madison Co. Bridge 502  
**For Week Ending:** 6/9/2018  
**Time Elapsed:** 51%  
**Date of Notice to Proceed:** 4/28/2017  
**Contractor:** Primco, Inc.  
**Owner:** Madison County

**Report No.:** 52  
**Calendar Completion Date:** 8/5/2019  
**Substantial Competition Date:** 6/5/2019  
**Contract Amount:** \$ 13,481,784.02  
**Incurred To Date:** \$ 8,053,303.69  
**Designer:** Beam, Longest, and Neff, LLC

**Contract Number:** B-36317  
**Project Number:** 1297202  
**Structure Number:** 502  
**Balance Remaining:** \$ 5,428,480.33  
**Project Complete Percent:** 60%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 3	No work on site.	Superstructure	Able to work on the controlling operation	8/8	Yes
Mon 4	Primco poured the interior rail. Michiana removed the northeast signal pole at Central Ave. E&B stringlined for paving.	Superstructure	Able to work on the controlling operation	8/8	Yes
Tues 5	Primco poured the interior rail. Michiana poured the northeast signal foundation.	Superstructure	Able to work on the controlling operation	8/8	Yes
Wed 6	Primco poured the interior rail. Michiana set handholes and poured the northwest signal foundation.	Superstructure	Able to work on the controlling operation	8/8	Yes
Thurs 7	Primco poured the interior rail. Michiana ran conduit and formed the ped foundations.	Superstructure	Able to work on the controlling operation	8/8	Yes
Fri 8	Primco poured the interior rail. Michiana relocated the existing signal cabinet and poured the new controller cabinet foundation. E&B canceled the paving.	Superstructure	Able to work on the controlling operation	8/8	Yes
Sat 9	Primco released the interior railing forms.	Superstructure	Able to work on the controlling operation	8/8	Yes

Distribution:

Original to Owner  
 cc: Project Engineer  
 cc: District File  
 cc: Contractor

CONTRACTOR ACCEPTANCE

\_\_\_\_\_  
Primco, Inc.

**REMARKS / PROJECTED WORK**

Primco will start forming and pouring the coping rail next week. E&B will pave the first base lift as soon as the weather permits. Once the base is paved, Primco will start pouring the curb and gutter.

Prepared by:

*Brian Rodgers*

\_\_\_\_\_  
Project Engineer

Approved \_\_\_\_\_, 2018

\_\_\_\_\_  
Madison County


# PROJECT PHOTOS



Primco rubbed the interior rail.



Primco formed the interior rail transition.

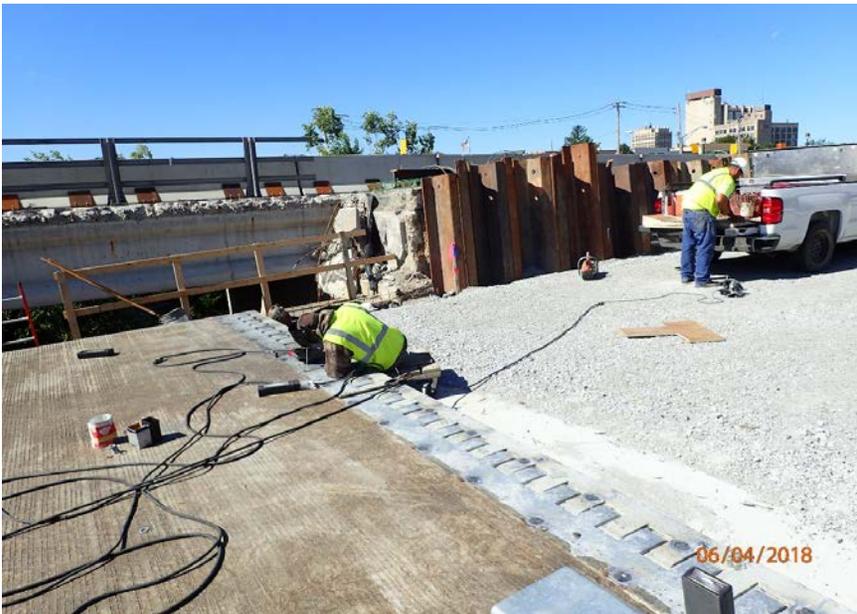

Primco fill welded the sliding tooth joint.B2:I33



Michiana rotated the signal arm at Central Ave.

# PROJECT PHOTOS



Primco poured the interior rail.



Michiana augured for the signal foundations.



Michiana poured the signal foundation.



Michiana installed conduit.
