

WEEKLY REPORT OF CONSTRUCTION ACTIVITIES

Project Name: Madison Co. Bridge 502
For Week Ending: 6/23/2018
Time Elapsed: 53%
Date of Notice to Proceed: 4/28/2017
Contractor: Primco, Inc.
Owner: Madison County

Report No.: 54
Calendar Completion Date: 8/5/2019
Substantial Competition Date: 6/5/2019
Contract Amount: \$ 13,481,784.02
Incurred To Date: \$ 8,138,864.79
Designer: Beam, Longest, and Neff, LLC

Contract Number: B-36317
Project Number: 1297202
Structure Number: 502
Balance Remaining: \$ 5,342,919.23
Project Complete Percent: 60%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 17	No work on site.	Superstructure	Able to work on the controlling operation	8/8	Yes
Mon 18	Primco poured the coping rail on the deck and on Wall 3A. The curb and gutter was completed on the east end.	Superstructure	Able to work on the controlling operation	8/8	Yes
Tues 19	Primco poured the coping rail on the deck and poured curb and gutter at Central Ave.	Superstructure	Able to work on the controlling operation	8/8	Yes
Wed 20	Primco poured curb and gutter on the west end and poured the coping rail on the deck.	Superstructure	Able to work on the controlling operation	8/8	Yes
Thurs 21	Primco poured coping rail on Wall 3 and on the deck. Curb and gutter was repoured on the west end. Crews left at noon due to rain.	Superstructure	Able to work on the controlling operation	5/8	Yes
Fri 22	Primco poured coping rail on the deck and formed curb and gutter for repouring.	Superstructure	Able to work on the controlling operation	8/8	Yes
Sat 23	No work on site.	Superstructure	Able to work on the controlling operation	8/8	Yes

Distribution:

Original to Owner
 cc: Project Engineer
 cc: District File
 cc: Contractor

CONTRACTOR ACCEPTANCE

Primco, Inc.

REMARKS / PROJECTED WORK

Primco will finish the curb and gutter on Monday. E&B will pave both the base and intermediate lifts of asphalt on Tuesday. C-Tech will start installing the steel PF-1 rail on Tuesday. The phase change is scheduled for July 2nd.

Prepared by:

Brian Rodgers

Project Engineer

Approved _____, 2018

Madison County

PROJECT PHOTOS



Primco poured the PF-1 rail on Wall 3A.



Primco poured the PF-1 rail on Wall 3.



Primco poured the curb and gutter on Central Ave.



Primco poured the PF-1 rail on the deck.


PROJECT PHOTOS



Primco formed the pier outlook.



Primco poured the PF-1 rail on the deck.

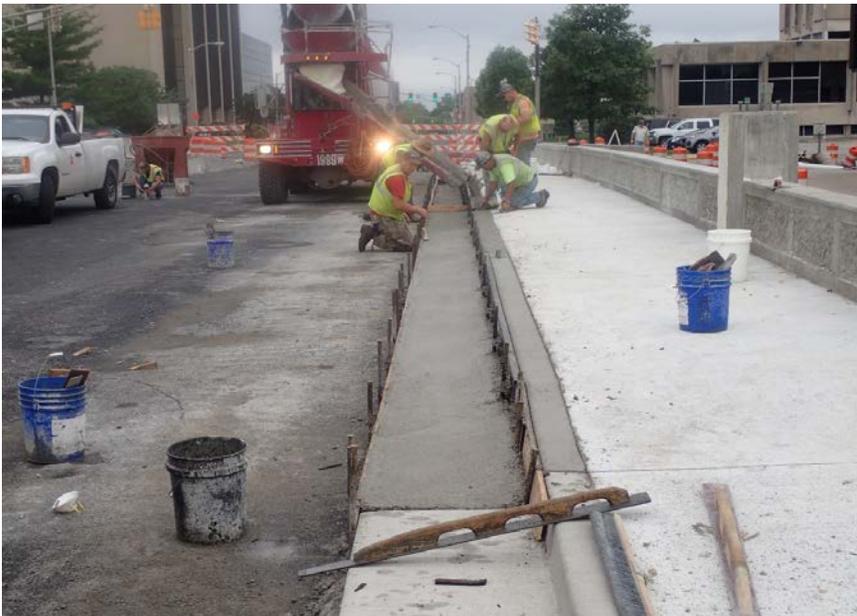

Primco poured curb and gutter on the west end.



Primco poured PF-1 rail on the deck.
