



WEEKLY REPORT OF CONSTRUCTION ACTIVITIES

Project Name: Madison Co. Bridge 502
For Week Ending: 8/11/2018
Time Elapsed: 60%
Date of Notice to Proceed: 4/28/2017
Contractor: Primco, Inc.
Owner: Madison County

Report No.: 61
Calendar Completion Date: 8/5/2019
Substantial Competition Date: 6/5/2019
Contract Amount: \$ 13,481,784.02
Incurred To Date: \$ 8,825,622.91
Designer: Beam, Longest, and Neff, LLC

Contract Number: B-36317
Project Number: 1297202
Structure Number: 502
Balance Remaining: \$ 4,656,161.11
Project Complete Percent: 65%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 5	No work on site.	Substructure	Able to work on the controlling operation	8/8	Yes
Mon 6	Primco pre-tied cap reinf, set the Pier 4 column forms, and removed an existing footing.	Substructure	Able to work on the controlling operation	8/8	Yes
Tues 7	Primco poured Pier 4 columns and removed an existing footing. IDEM site visit due to a dust complaint. No violations found.	Substructure	Able to work on the controlling operation	8/8	Yes
Wed 8	Primco wrecked the Pier 4 column forms and pre-tied cap reinf.	Substructure	Able to work on the controlling operation	8/8	Yes
Thurs 9	Primco set the Pier 3 column forms, pre-tied cap reinf, and added stone to the causeway entrance.	Substructure	Able to work on the controlling operation	8/8	Yes
Fri 10	Primco poured the Pier 3 columns and placed the falsework for the Pier 4 cap.	Substructure	Able to work on the controlling operation	8/8	Yes
Sat 11	Primco wrecked the Pier 3 columns and moved the causeway riprap.	Substructure	Able to work on the controlling operation	8/8	Yes

Distribution:
 Original to Owner
 cc: Project Engineer
 cc: District File
 cc: Contractor

CONTRACTOR ACCEPTANCE

Primco, Inc.

REMARKS / PROJECTED WORK

Primco will start driving the Pier 5 piling on Monday. The Pier 5 footers will poured towards the end of the week.

Prepared by:

Brian Rodgers

Project Engineer

Approved _____, 2018

Madison County

PROJECT PHOTOS




Primco set the Pier 4 column forms.



Primco adjusted the column reinforcing.



Primco poured the Pier 4 columns.

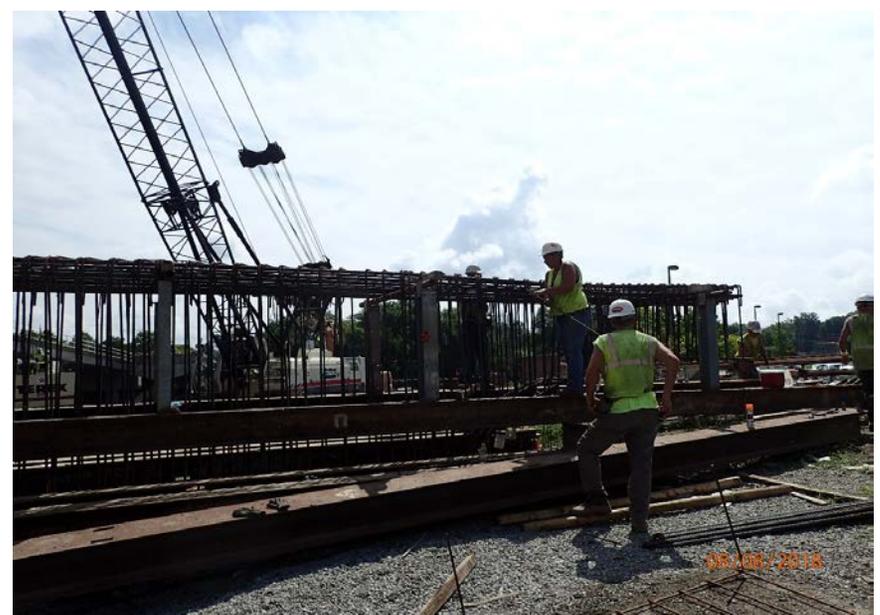

Primco pre-tied the pier cap reinforcing.

PROJECT PHOTOS



Primco wrapped the pier columns.



Primco poured the Pier 3 columns.



Primco poured the Pier 3 columns.



Primco placed the Pier 4 cap falsework.
