

WEEKLY REPORT OF CONSTRUCTION ACTIVITIES



Project Name: Madison Co. Bridge 502
For Week Ending: 10/6/2018
Time Elapsed: 67%
Date of Notice to Proceed: 4/28/2017
Contractor: Primco, Inc.
Owner: Madison County

Report No.: 69
Calendar Completion Date: 8/5/2019
Substantial Competition Date: 6/5/2019
Contract Amount: \$ 13,481,784.02
Incurred To Date: \$ 9,539,566.80
Designer: Beam, Longest, and Neff, LLC

Contract Number: B-36317
Project Number: 1297202
Structure Number: 502
Balance Remaining: \$ 3,942,217.22
Project Complete Percent: 71%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 30	No work on site.	Pier 6/Bent 7	Able to work on the controlling operation	8/8	Yes
Mon 1	Primco tied the Pier 6 reinforcing, formed the Pier 6 cap, and moved in the 80ton crane.	Pier 6/Bent 7	Able to work on the controlling operation	8/8	Yes
Tues 2	Primco drove sheeting at Wall 1A and set the Pier 6 reinforcing into the cap.	Pier 6/Bent 7	Able to work on the controlling operation	8/8	Yes
Wed 3	Primco formed and poured the Pier 6 cap, moved in the 165ton crane, and removed portions of the south levee wall.	Pier 6/Bent 7	Able to work on the controlling operation	8/8	Yes
Thurs 4	Primco formed the south levee wall and drove sheeting at Wall 1A.	Pier 6/Bent 7	Able to work on the controlling operation	8/8	Yes
Fri 5	Primco finished the sheeting at Wall 1A, formed the south levee wall, and backfilled Bent 7.	Pier 6/Bent 7	Delay in the controlling operation. Primco backfilled the arch footing hole. All work associated with the arch footing removal is complete. Eight total days granted for the removal.	0/8	No
Sat 6	Primco drove the Bent 1 piles, spliced the piles, and drilled the anchor holes for Wall 1A.	Pier 6	Able to work on the controlling operation	8/8	Yes

Distribution:

- Original to Owner
- cc: Project Engineer
- cc: District File
- cc: Contractor

CONTRACTOR ACCEPTANCE

Primco, Inc.

REMARKS / PROJECTED WORK

Primco will finish the piling at Bent 1 on Monday. All the piling on the project will be complete. Primco will pour the south levee wall on Monday. Primco will start setting the articulating block mattress at Bent 7 next week. The west end will be prepped for the MSE wall.

Prepared by:

Brian Rodgers

Project Engineer

Approved _____, 2018

Madison County

PROJECT PHOTOS



Primco drove the sheeting for Wall 1A.



Primco placed the Pier 6 cap reinforcing.



Primco placed the Pier 6 cap reinforcing.



Primco poured the Pier 6 cap.

PROJECT PHOTOS



Primco finished the Pier 6 cap.



Primco placed reinforcing and formed the south levee wall.



Primco drove sheeting for Wall 1A.



Primco drove sheeting for Wall 1A.

PROJECT PHOTOS




Primco drilled the anchor bolt holes for Wall 1A.



Primco drove piling at Bent 1.



Primco spliced the piling at Bent 1.

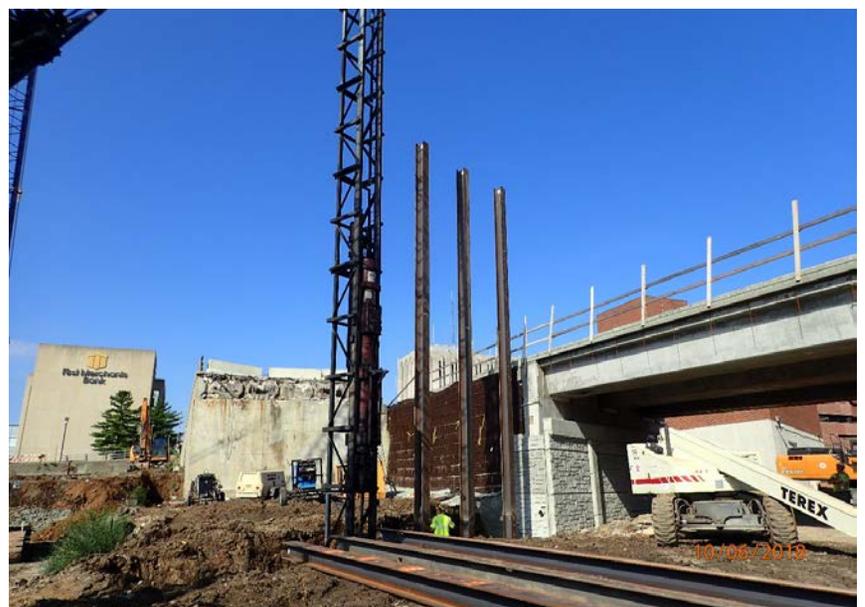

Primco drove piling at Bent 1.
