

# WEEKLY REPORT OF CONSTRUCTION ACTIVITIES

**Project Name:** Madison Co. Bridge 502  
**For Week Ending:** 10/20/2018  
**Time Elapsed:** 69%  
**Date of Notice to Proceed:** 4/28/2017  
**Contractor:** Primco, Inc.  
**Owner:** Madison County

**Report No.:** 71  
**Calendar Completion Date:** 8/5/2019  
**Substantial Competition Date:** 6/5/2019  
**Contract Amount:** \$ 13,481,784.02  
**Incurred To Date:** \$ 9,777,369.36  
**Designer:** Beam, Longest, and Neff, LLC

**Contract Number:** B-36317  
**Project Number:** 1297202  
**Structure Number:** 502  
**Balance Remaining:** \$ 3,704,414.66  
**Project Complete Percent:** 73%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 14	No work on site.	Art Block Mat at Bent 7	Able to work on the controlling operation	8/8	Yes
Mon 15	Primco constructed Wall 2 and placed the articulating block mattress at Bent 7.	Art Block Mat at Bent 7	Able to work on the controlling operation	8/8	Yes
Tues 16	Primco constructed Wall 2, grouted the block mattress seams at Bent 7, extended the Phase 1 deck drains, and prepped the trail under the east end of the bridge.	Art Block Mat at Bent 7	Able to work on the controlling operation	8/8	Yes
Wed 17	Primco constructed Wall 2, formed the trail under the east end of the bridge, and drove sheeting at Wall 4.	Beams - Span C to F	Able to work on the controlling operation	8/8	Yes
Thurs 18	Primco poured the trail under the east end of the bridge, set the bearing pads, drove sheeting at Wall 4, and constructed Wall 2.	Beams - Span C to F	Able to work on the controlling operation	8/8	Yes
Fri 19	Primco constructed Wall 2, finished the sheeting at Wall 4, and removed the trail forms. AML&P supported the pole at Wall 4.	Beams - Span C to F	Able to work on the controlling operation	8/8	Yes
Sat 20	Primco constructed Wall 2, backfilled the pile sleeves, and built crane pads for the beam setting operation.	Beams - Span C to F	Able to work on the controlling operation	8/8	Yes

Distribution:

- Original to Owner
- cc: Project Engineer
- cc: District File
- cc: Contractor

CONTRACTOR ACCEPTANCE

\_\_\_\_\_  
Primco, Inc.

**REMARKS / PROJECTED WORK**

Primco will set the bridge beams from Span C to F from October 23rd to the 26th. The bridge will be closed from 9am to 4pm each day.

Prepared by:

*Brian Rodgers*

\_\_\_\_\_  
Project Engineer

Approved \_\_\_\_\_, 2018

\_\_\_\_\_  
Madison County

# PROJECT PHOTOS




Primco set the articulating block mattress at Bent 7.



Primco set the articulating block mattress at Bent 7.



Primco set panels at Wall 2.

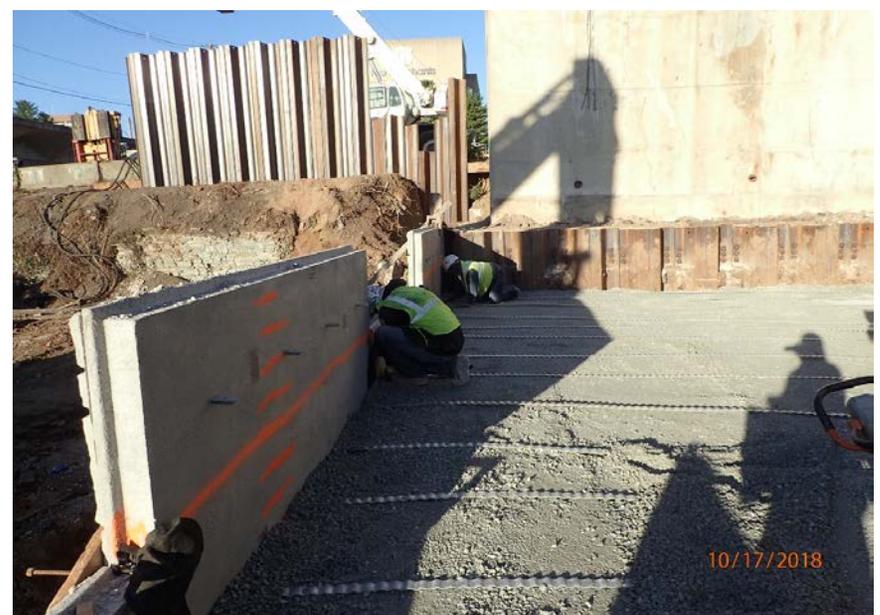

Primco installed straps at Wall 2.

# PROJECT PHOTOS




Primco extended the deck drains.



Primco poured the trail under the east end of the bridge.



Primco set panels at Wall 2.

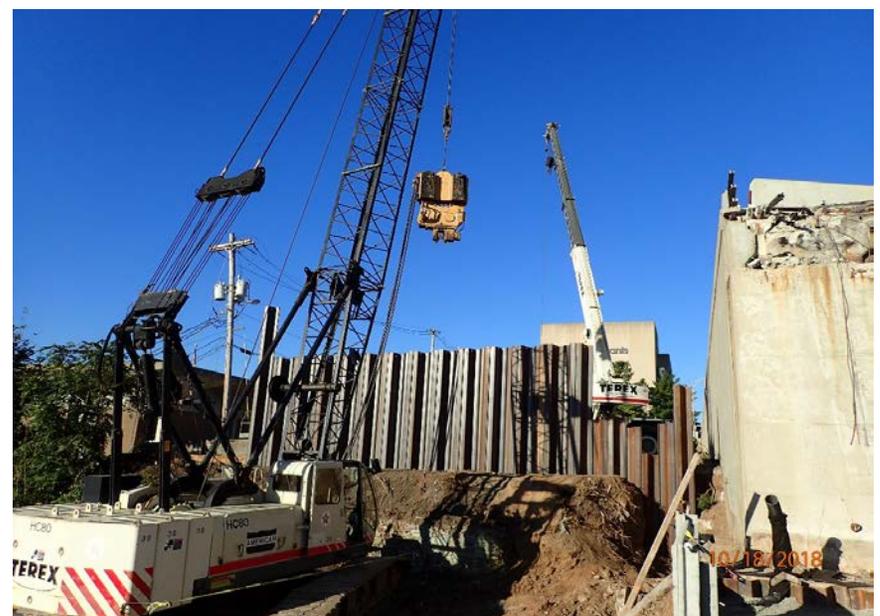

Primco drove sheeting at Wall 4.

# PROJECT PHOTOS



Primco backfilled Wall 2.



Primco constructed Wall 2.



Primco filled the pile sleeves.



Primco built crane pads to set the beams.
