



WEEKLY REPORT OF CONSTRUCTION ACTIVITIES

Project Name: Madison Co. Bridge 502
For Week Ending: 10/27/2018
Time Elapsed: 70%
Date of Notice to Proceed: 4/28/2017
Contractor: Primco, Inc.
Owner: Madison County

Report No.: 72
Calendar Completion Date: 8/5/2019
Substantial Competition Date: 6/5/2019
Contract Amount: \$ 13,481,784.02
Incurred To Date: \$ 10,120,524.35
Designer: Beam, Longest, and Neff, LLC

Contract Number: B-36317
Project Number: 1297202
Structure Number: 502
Balance Remaining: \$ 3,361,259.67
Project Complete Percent: 75%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 21	No work on site.	Beams - Span C to F	Able to work on the controlling operation	8/8	Yes
Mon 22	Primco constructed Wall 2, prepped for beams, pre-tied the Bent 1 reinforcing, and excavated at Wall 4.	Beams - Span C to F	Able to work on the controlling operation	8/8	Yes
Tues 23	Primco set the Span E beams, formed Bent 1, and removed the west abutment.	Beams - Span C to F	Able to work on the controlling operation	8/8	Yes
Wed 24	Primco set the Span F beams, formed Bent 1, and removed the west abutment.	Beams - Span C to F	Able to work on the controlling operation	8/8	Yes
Thurs 25	Primco set the Span D beams, welded the beams to the bearing assemblies, installed the strand clamps, removed the west abutment, and formed Bent 1.	Beams - Span C to F	Able to work on the controlling operation	8/8	Yes
Fri 26	Primco set the Span C beams, poured Bent 1, laid out the screed grades, and tied the Bent 7 end diaphragm reinforcing.	Beams - Span C to F	Able to work on the controlling operation	8/8	Yes
Sat 27	Primco tied the Bent 7 end diaphragm reinforcing, formed the diaphragms, and welded the deck pan angle iron.	Deck - East Half	Able to work on the controlling operation	8/8	Yes

Distribution:
 Original to Owner
 cc: Project Engineer
 cc: District File
 cc: Contractor

REMARKS / PROJECTED WORK

Primco will continue to form the deck next week.

CONTRACTOR ACCEPTANCE

Primco, Inc.

Prepared by:

Brian Rodgers

Project Engineer

Approved _____, 2018

Madison County

PROJECT PHOTOS



Primco constructed MSE Wall 2.



Primco set the pre-tied cage at Bent 1.



Primco set the Span E beams.



Primco formed Bent 1.

PROJECT PHOTOS



Primco set the Span F beams.



Primco welded the beams to the bearing assemblies.



Primco set the Span D beams.



Primco removed the west abutment.

PROJECT PHOTOS




Primco poured Bent 1.



Primco set the Span C beams.



Primco formed the Bent 7 end diaphragm.

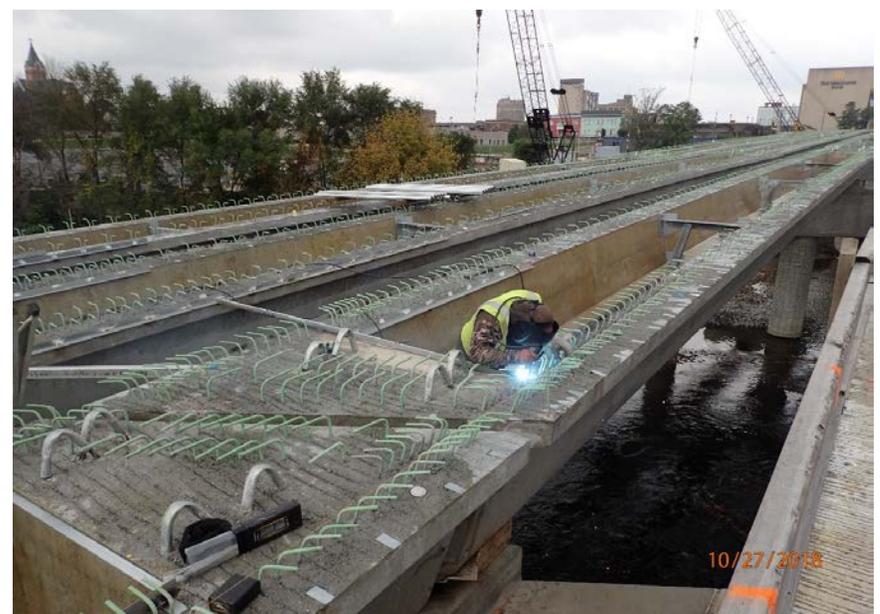

Primco welded the deck pan angle iron.
