

WEEKLY REPORT OF CONSTRUCTION ACTIVITIES



Project Name: Madison Co. Bridge 502
For Week Ending: 11/3/2018
Time Elapsed: 71%
Date of Notice to Proceed: 4/28/2017
Contractor: Primco, Inc.
Owner: Madison County

Report No.: 73
Calendar Completion Date: 8/5/2019
Substantial Competition Date: 6/5/2019
Contract Amount: \$ 13,481,784.02
Incurred To Date: \$ 10,133,362.45
Designer: Beam, Longest, and Neff, LLC

Contract Number: B-36317
Project Number: 1297202
Structure Number: 502
Balance Remaining: \$ 3,348,421.57
Project Complete Percent: 75%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 28	No work on site.	Deck - East Half	Able to work on the controlling operation	8/8	Yes
Mon 29	Primco wrecked the Bent 1 forms, formed the Wall 2 coping, formed the Bent 7 diaphragm, and welded angle iron for the deck pans.	Deck - East Half	Able to work on the controlling operation	8/8	Yes
Tues 30	Primco poured the Bent 7 diaphragm, formed the Pier 6 diaphragm, poured the Wall 2 coping, and welded angle iron for the deck pans.	Deck - East Half	Able to work on the controlling operation	8/8	Yes
Wed 31	Primco welded angle iron, installed deck pans, and installed coping falsework. Bertsch Frank shot the Phase 1 beam deflections.	Deck - East Half	Able to work on the controlling operation	8/8	Yes
Thurs 1	No work on site due to weather.	Deck - East Half	Weather	0/8	No
Fri 2	Primco wrecked the Bent 7 diaphragm, formed the pier diaphragms, and installed deck pans.	Deck - East Half	Able to work on the controlling operation	8/8	Yes
Sat 3	Primco installed deck pans and formed the pier diaphragms.	Deck - East Half	Able to work on the controlling operation	8/8	Yes

Distribution:

- Original to Owner
- cc: Project Engineer
- cc: District File
- cc: Contractor

CONTRACTOR ACCEPTANCE

Primco, Inc.

REMARKS / PROJECTED WORK

The Span A and B beams will be delivered on November 6th and 7th. Primco will continue to form the deck next week.

Prepared by:

Brian Rodgers

Project Engineer

Approved _____, 2018

Madison County


PROJECT PHOTOS



Primco removed the west abutment.



Primco formed the Bent 7 diaphragm.

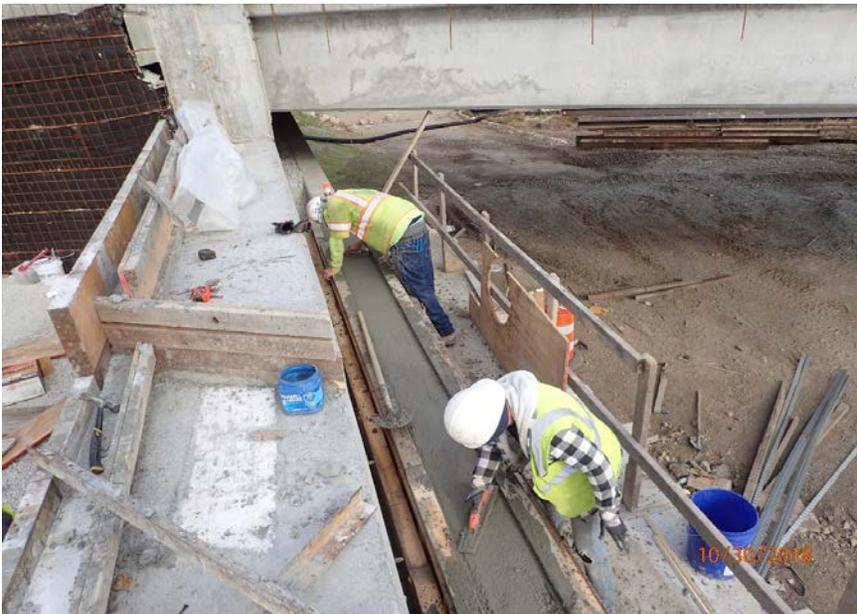

Primco poured the Wall 2 coping.



Primco welded the deck pan angle iron.

PROJECT PHOTOS



Primco welded the deck pan angle iron.



Primco installed the deck pans.



Primco installed the deck pans.



Primco installed the deck pans.
