



# WEEKLY REPORT OF CONSTRUCTION ACTIVITIES

**Project Name:** Madison Co. Bridge 502  
**For Week Ending:** 11/10/2018  
**Time Elapsed:** 72%  
**Date of Notice to Proceed:** 4/28/2017  
**Contractor:** Primco, Inc.  
**Owner:** Madison County

**Report No.:** 74  
**Calendar Completion Date:** 8/5/2019  
**Substantial Competition Date:** 6/5/2019  
**Contract Amount:** \$ 13,481,784.02  
**Incurred To Date:** \$ 10,310,593.21  
**Designer:** Beam, Longest, and Neff, LLC

**Contract Number:** B-36317  
**Project Number:** 1297202  
**Structure Number:** 502  
**Balance Remaining:** \$ 3,171,190.81  
**Project Complete Percent:** 76%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 4	No work on site.	Deck - East Half	Able to work on the controlling operation	8/8	Yes
Mon 5	Primco formed the pier diaphragms, installed coping and phase line falsework, and installed deck pans.	Deck - East Half	Able to work on the controlling operation	8/8	Yes
Tues 6	Primco set Span B beams, installed deck pans, formed the pier diaphragms, and installed coping and phase line falsework.	Deck - East Half	Able to work on the controlling operation	8/8	Yes
Wed 7	Primco set the Span A beams, installed deck pans, formed the pier diaphragms, and placed the coping and phase line falsework.	Deck - East Half	Able to work on the controlling operation	8/8	Yes
Thurs 8	Primco installed the deck pans, formed the pier diaphragms, and installed coping and phase line falsework.	Deck - East Half	Able to work on the controlling operation	8/8	Yes
Fri 9	Primco installed the deck pans, formed the pier diaphragms, installed coping and phase line falsework, and tied the pier diaphragm reinforcing.	Deck - East Half	Able to work on the controlling operation	8/8	Yes
Sat 10	Primco installed the deck pans, formed the pier diaphragms, and installed coping and phase line falsework.	Deck - East Half	Able to work on the controlling operation	8/8	Yes

Distribution:  
 Original to Owner  
 cc: Project Engineer  
 cc: District File  
 cc: Contractor

CONTRACTOR ACCEPTANCE

\_\_\_\_\_  
Primco, Inc.

**REMARKS / PROJECTED WORK**

Primco will continue to form the deck. Harmon will start installing bridge deck reinforcing on Wednesday.

Prepared by:

*Brian Rodgers*

\_\_\_\_\_  
Project Engineer

Approved \_\_\_\_\_, 2018

\_\_\_\_\_  
Madison County

# PROJECT PHOTOS



View from the Blue Bridge



Primco installed deck pans and the phaseline falsework.



Primco set the Span B beams.



Primco welded the deck pan angle iron.

# PROJECT PHOTOS




Primco set the Span A beams.



Primco set the span A beams.



Primco set the Span A beams.

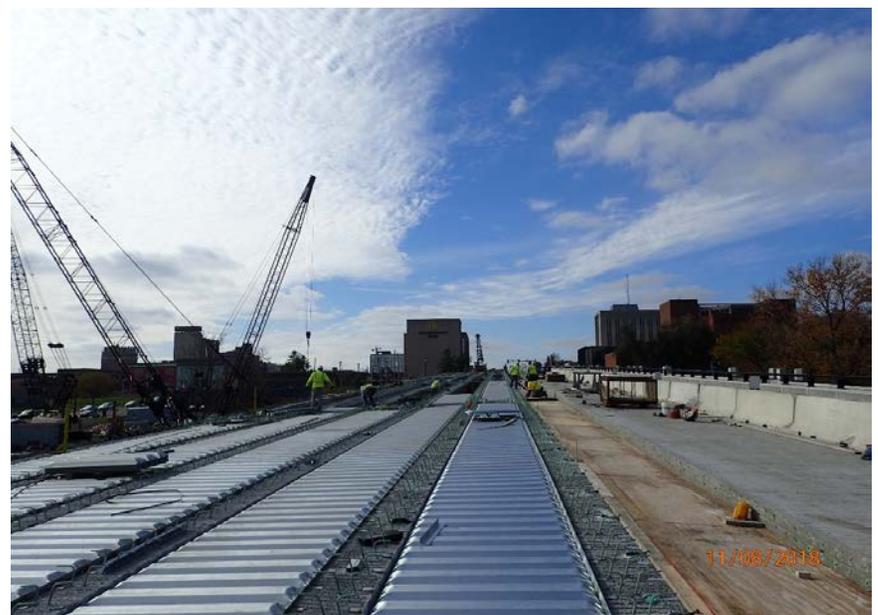

Primco installed deck pans.

# PROJECT PHOTOS



Primco installed the coping falsework.



Primco installed the phase line falsework.



Primco installed the deck pans.



3D installed filter sock and added stone to the filter berm.
