

WEEKLY REPORT OF CONSTRUCTION ACTIVITIES



Project Name: Madison Co. Bridge 502
For Week Ending: 11/17/2018
Time Elapsed: 73%
Date of Notice to Proceed: 4/28/2017
Contractor: Primco, Inc.
Owner: Madison County

Report No.: 75
Calendar Completion Date: 8/5/2019
Substantial Competition Date: 6/5/2019
Contract Amount: \$ 13,481,784.02
Incurred To Date: \$ 10,565,481.09
Designer: Beam, Longest, and Neff, LLC

Contract Number: B-36317
Project Number: 1297202
Structure Number: 502
Balance Remaining: \$ 2,916,302.93
Project Complete Percent: 78%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 11	No work on site.	Deck - East Half	Able to work on the controlling operation	8/8	Yes
Mon 12	Primco installed deck pans, coping falsework, and diaphragm reinforcing.	Deck - East Half	Able to work on the controlling operation	8/8	Yes
Tues 13	Harmon laid out the reinforcing bars. Primco installed deck pans, coping falsework, phaseline falsework, and diaphragm reinforcing.	Deck - East Half	Able to work on the controlling operation	8/8	Yes
Wed 14	Harmon tied the deck reinforcing. Primco installed threaded tie bars, diaphragm reinforcing, diaphragm forms, and coping forms.	Deck - East Half	Able to work on the controlling operation	8/8	Yes
Thurs 15	The reinforcing and falsework was covered in ice. Primco and Harmon left the site at 8am.	Deck - East Half	Weather	0/8	No
Fri 16	Primco prepped the deck. Harmon tied the deck reinforcing.	Deck - East Half	Able to work on the controlling operation	12/12	Yes
Sat 17	Primco prepped the deck. Harmon tied the deck reinforcing. Michiana installed the lighting conduit.	Deck - East Half	Able to work on the controlling operation	9/9	Yes

Distribution:
 Original to Owner
 cc: Project Engineer
 cc: District File
 cc: Contractor

REMARKS / PROJECTED WORK

Prepared by: Brian Rodgers
 Project Engineer

Approved _____, 2018

Madison County

CONTRACTOR ACCEPTANCE

Primco, Inc.

PROJECT PHOTOS



Primco installed the deck pans.



Primco installed the coping forms.



Primco installed the diaphragm reinforcing.



Primco installed the threaded tie bars.

PROJECT PHOTOS



Harmon tied the deck reinforcing.



Harmon tied the deck reinforcing.



Harmon tied the deck reinforcing.



Harmon tied the deck reinforcing.



WEEKLY REPORT OF CONSTRUCTION ACTIVITIES

Project Name: Madison Co. Bridge 502
For Week Ending: 11/17/2018
Time Elapsed: 74%
Date of Notice to Proceed: 4/28/2017
Contractor: Primco, Inc.
Owner: Madison County

Report No.: 76
Calendar Completion Date: 8/5/2019
Substantial Competition Date: 6/5/2019
Contract Amount: \$ 13,481,784.02
Incurred To Date: \$ 10,565,481.09
Designer: Beam, Longest, and Neff, LLC

Contract Number: B-36317
Project Number: 1297202
Structure Number: 502
Balance Remaining: \$ 2,916,302.93
Project Complete Percent: 78%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 18	No work on site.	Deck - East Half	Able to work on the controlling operation	8/8	Yes
Mon 19	Primco set the screed rails and formed the Bent 1 diaphragm. Harmon tied the deck reinforcing.	Deck - East Half	Able to work on the controlling operation	9/9	Yes
Tues 20	Primco completed the dry run, poured the Bent 1 diaphragm, and installed temperature sensors in the bridge deck. Harmon tied the reinforcing steel.	Deck - East Half	Able to work on the controlling operation	8/8	Yes
Wed 21	Primco poured the east half of the deck. RL McCoy pumped the concrete.	Deck - East Half	Able to work on the controlling operation	8/8	Yes
Thurs 22	Primco removed the beam forms and placed the beams on the bridge deck.	Deck - West Half	Holiday	8/8	Yes
Fri 23	Primco checked the temperatures sensors.	Deck - West Half	Holiday	8/8	Yes
Sat 24	Primco checked the temperatures sensors and opened the eastbound lane to traffic.	Deck - West Half	Holiday	8/8	Yes

Distribution:
 Original to Owner
 cc: Project Engineer
 cc: District File
 cc: Contractor

REMARKS / PROJECTED WORK

CONTRACTOR ACCEPTANCE

Primco, Inc.

Prepared by:

Brian Rodgers

Project Engineer

Approved _____, 2018

Madison County

PROJECT PHOTOS



Harmon tied the deck reinforcing.



Primco installed the screed rails.



Primco poured the Bent 1 diaphragm.



Primco prepped the deck.

PROJECT PHOTOS



Primco completed the dry run.



Primco poured the deck.



Primco tined the deck.



RL McCoy pumped the concrete.

PROJECT PHOTOS



Primco poured the bridge deck.



Primco checked the beam deflection.



Primco poured the deck.



Primco started covering the deck.



WEEKLY REPORT OF CONSTRUCTION ACTIVITIES

Project Name: Madison Co. Bridge 502
For Week Ending: 12/1/2018
Time Elapsed: 75%
Date of Notice to Proceed: 4/28/2017
Contractor: Primco, Inc.
Owner: Madison County

Report No.: 77
Calendar Completion Date: 8/5/2019
Substantial Competition Date: 6/5/2019
Contract Amount: \$ 13,481,784.02
Incurred To Date: \$ 11,149,406.54
Designer: Beam, Longest, and Neff, LLC

Contract Number: B-36317
Project Number: 1297202
Structure Number: 502
Balance Remaining: \$ 2,332,377.48
Project Complete Percent: 83%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 25	Primco checked the temperature sensors.	Deck - West Half	Holiday	8/8	Yes
Mon 26	Primco prepped the west half of the deck. Harmon tied the bridge deck reinforcing.	Deck - West Half	Able to work on the controlling operation	8/8	Yes
Tues 27	Primco prepped the west half of the deck and placed stone at Bent 1. Harmon tied the bridge deck reinforcing.	Deck - West Half	Able to work on the controlling operation	8/8	Yes
Wed 28	Primco set the screed rails. Harmon tied the deck reinforcing. Michiana installed the lighting conduit.	Deck - West Half	Able to work on the controlling operation	8/8	Yes
Thurs 29	Primco completed the dry run, installed temperature sensors, and installed the helical piles at Wall 4. Harmon completed the deck reinforcing.	Deck - West Half	Able to work on the controlling operation	8/8	Yes
Fri 30	Primco poured the west half of the deck.	Deck - West Half	Able to work on the controlling operation	8/8	Yes
Sat 1	Primco checked the deck covering and removed the test beam forms.	Deck - West Half	Able to work on the controlling operation	8/8	Yes

Distribution:
 Original to Owner
 cc: Project Engineer
 cc: District File
 cc: Contractor

REMARKS / PROJECTED WORK

Primco will start prepping for the coping rail next week.

CONTRACTOR ACCEPTANCE

Primco, Inc.

Prepared by:

Brian Rodgers

Project Engineer

Approved _____, 2018

Madison County

PROJECT PHOTOS



Primco formed the bulk head.



Harmon tied the deck reinforcing.



Harmon tied the deck reinforcing.



Primco applied the test load to the helical piles at Wall 4.

PROJECT PHOTOS



Primco adjusted the deck drain.



Primco completed the dry run.



Primco poured the deck.



Primco poured the deck.

PROJECT PHOTOS




Primco poured the bridge deck.



Primco tined the deck.



Primco poured the deck.

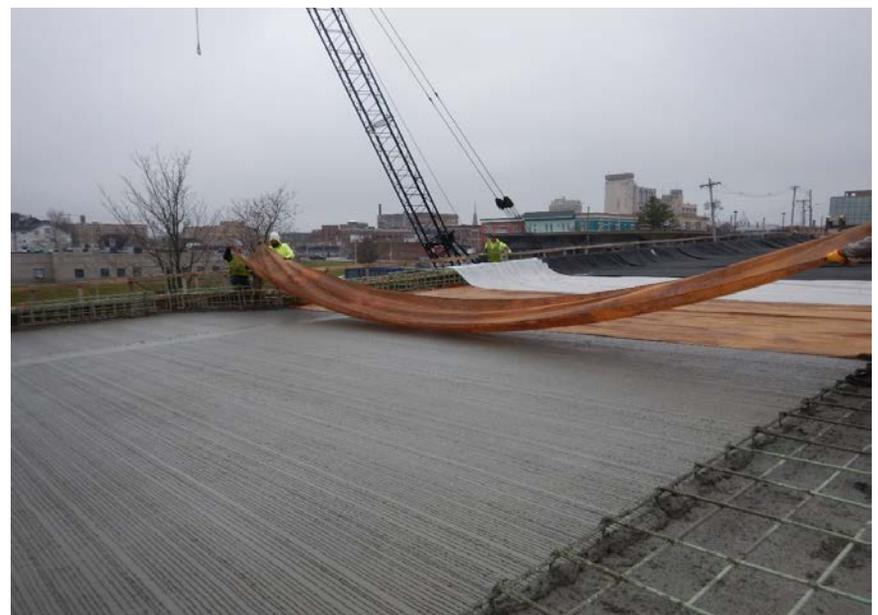

Primco started covering the deck.
