



WEEKLY REPORT OF CONSTRUCTION ACTIVITIES

Project Name: Madison Co. Bridge 502
For Week Ending: 12/22/2018
Time Elapsed: 78%
Date of Notice to Proceed: 4/28/2017
Contractor: Primco, Inc.
Owner: Madison County

Report No.: 80
Calendar Completion Date: 8/5/2019
Substantial Competition Date: 6/5/2019
Contract Amount: \$ 13,481,784.02
Incurred To Date: \$ 11,313,570.24
Designer: Beam, Longest, and Neff, LLC

Contract Number: B-36317
Project Number: 1297202
Structure Number: 502
Balance Remaining: \$ 2,168,213.78
Project Complete Percent: 84%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 16	No work on site.	Railing	Able to work on the controlling operation	8/8	Yes
Mon 17	Primco poured a section of coping rail and installed the interior railing bars. 3D finished the excavation for Wall 1 and removed concrete pavement at Wall 4.	Railing	Able to work on the controlling operation	8/8	Yes
Tues 18	Primco poured a section of coping rail and installed the interior railing bars. 3D excavated at Wall 4 and placed erosion control stone.	Railing	Able to work on the controlling operation	8/8	Yes
Wed 19	Primco poured a section of coping rail and installed the interior railing bars. 3D hauled off stockpiled soil and removed the retaining wall along the jail drive.	Railing	Able to work on the controlling operation	8/8	Yes
Thurs 20	Primco formed the coping rail, installed interior rail reinf, and cleaned site. 3D hauled off stockpiled soil.	Railing	Able to work on the controlling operation	8/8	Yes
Fri 21	3D graded the Pier 2 slope and hauled off excess soil.	Railing	Able to work on the controlling operation	8/8	Yes
Sat 22	No work on site.	Railing	Able to work on the controlling operation	8/8	Yes

Distribution:

- Original to Owner
- cc: Project Engineer
- cc: District File
- cc: Contractor

CONTRACTOR ACCEPTANCE

Primco, Inc.

REMARKS / PROJECTED WORK

3D will return to work on January 3rd. Primco will return on January 7th.

Prepared by:

Brian Rodgers

Project Engineer


Approved _____, 2018

Madison County

PROJECT PHOTOS



3D excavated for Wall 1.

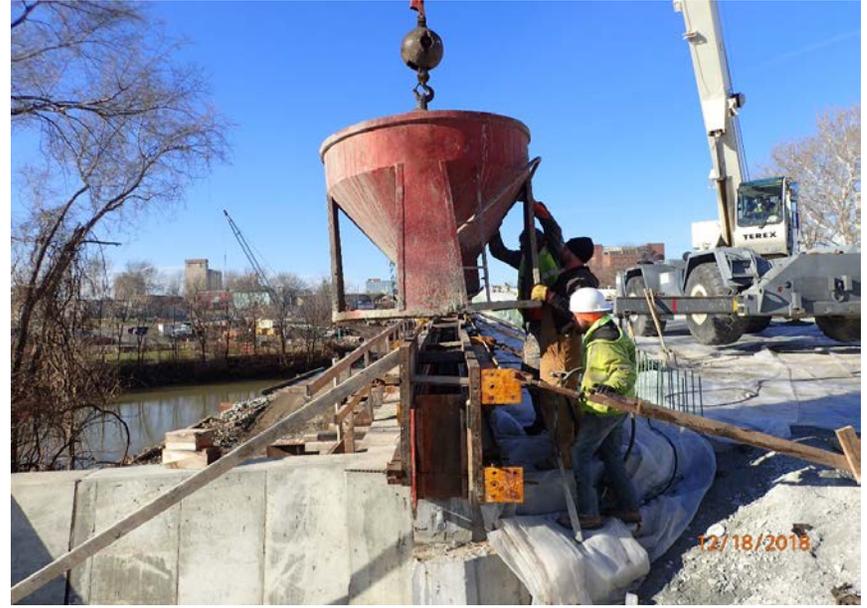

Primco poured a section of coping rail.



Primco installed the interior rail reinforcing.



3D excavated for Wall 4.

PROJECT PHOTOS



Primco poured the pier outlook railing.



Primco epoxied the interior rail bars.



3D hauled stockpiled soil off site.



3D graded the Pier 2 slope.
