

# WEEKLY REPORT OF CONSTRUCTION ACTIVITIES



**Project Name:** Madison Co. Bridge 502  
**For Week Ending:** 1/26/2019  
**Time Elapsed:** 83%  
**Date of Notice to Proceed:** 4/28/2017  
**Contractor:** Primco, Inc.  
**Owner:** Madison County

**Report No.:** 85  
**Calendar Completion Date:** 8/5/2019  
**Substantial Competition Date:** 6/14/2019  
**Contract Amount:** \$ 13,481,784.02  
**Incurred To Date:** \$ 11,491,070.62  
**Designer:** Beam, Longest, and Neff, LLC

**Contract Number:** B-36317  
**Project Number:** 1297202  
**Structure Number:** 502  
**Balance Remaining:** \$ 1,990,713.40  
**Project Complete Percent:** 85%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 20	No work on site.	Railing	Able to work on the controlling operation	8/8	Yes
Mon 21	No work on site. Primco held safety training for their employees.	Railing	Able to work on the controlling operation	8/8	Yes
Tues 22	Primco poured coping and interior rail. The south end of Wall 4 was formed and poured.	Railing	Able to work on the controlling operation	8/8	Yes
Wed 23	Primco left the site at 8am due to rain.	Railing	Weather	0/8	No
Thurs 24	Primco poured interior rail and coping on Wall 1A. The old retaining wall concrete at Wall 1 was removed.	Railing	Able to work on the controlling operation	8/8	Yes
Fri 25	Primco drilled holes into the existing footing for the Wall 1 leveling pad reinforcing and installed the reinforcing bars.	Railing	Able to work on the controlling operation	8/8	Yes
Sat 26	No work on site.	Railing	Able to work on the controlling operation	8/8	Yes

Distribution:  
 Original to Owner  
 cc: Project Engineer  
 cc: District File  
 cc: Contractor

**REMARKS / PROJECTED WORK**

Primco will pour the Wall 1 leveling pad on Monday. Due to the low temperatures, Primco will not work on Tuesday, Wednesday, or Thursday. The foreman will check on the heaters during these days.

Prepared by: Brian Rodger  
 Project Engineer

Approved \_\_\_\_\_, 2019

\_\_\_\_\_ Madison County

CONTRACTOR ACCEPTANCE

\_\_\_\_\_  
Primco, Inc.

# PROJECT PHOTOS



Primco removed the old retaining wall.



Primco poured the Pier 2 outlook.



Primco finished pouring the face of Wall 4.



Primco removed the forms and blanketed Wall 4.

# PROJECT PHOTOS




Primco poured the coping for Wall 1A.



Wall 4



Primco removed concrete for Wall 1.

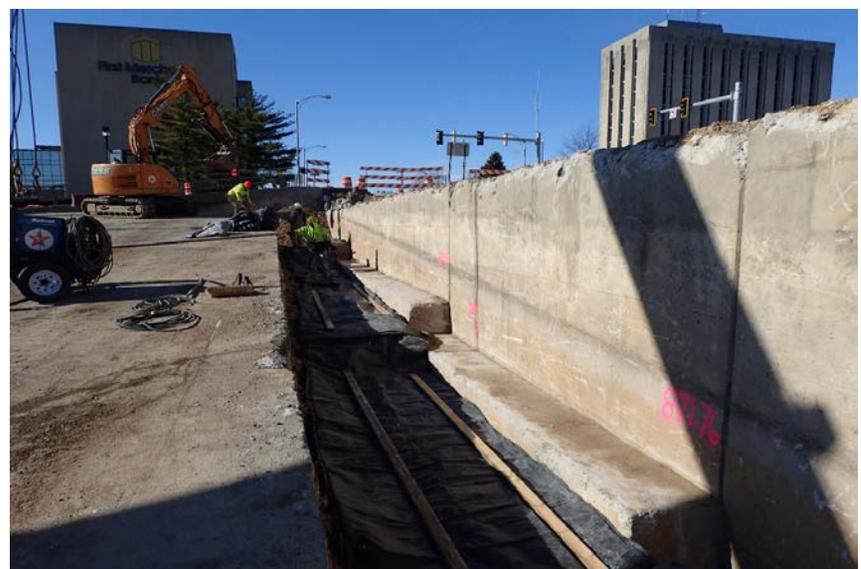

Primco covered the ground at Wall 1 to keep it from freezing.
