

WEEKLY REPORT OF CONSTRUCTION ACTIVITIES



Project Name: Madison Co. Bridge 502
For Week Ending: 8/17/2019
Time Elapsed: 100%
Date of Notice to Proceed: 4/28/2017
Contractor: Primco, Inc.
Owner: Madison County

Report No.: 114
Calendar Completion Date: 8/5/2019
Substantial Competition Date: 6/18/2019
Contract Amount: \$ 13,748,931.15
Incurred To Date: \$ 13,585,600.94
Designer: Beam, Longest, and Neff, LLC

Contract Number: B-36317
Project Number: 1297202
Structure Number: 502
Balance Remaining: \$ 163,330.21
Project Complete Percent: 99%

Day and Date	Work in Progress	Current Controlling Operations	Reasons for Reporting As a Work Day or Non-Work Day	Fraction of Day Workable	Work Days Charged
Sun 11	No work on site.	Lighting	Able to work on the controlling operation	8/8	Yes
Mon 12	No work on site.	Lighting	Able to work on the controlling operation	8/8	Yes
Tues 13	Michiana installed the north side bridge poles.	Lighting	Able to work on the controlling operation	8/8	Yes
Wed 14	Michiana installed the south side bridge poles, the temporary path poles, and all the bridge fixtures. Slussers watered the sod.	Lighting	Able to work on the controlling operation	8/8	Yes
Thurs 15	Michiana installed the temporary path fixtures. Ribbon Cutting Ceremony was held.	Lighting	Able to work on the controlling operation	8/8	Yes
Fri 16	No work on site.	Lighting	Able to work on the controlling operation	8/8	Yes
Sat 17	No work on site.	Lighting	Able to work on the controlling operation	8/8	Yes

Distribution:
 Original to Owner
 cc: Project Engineer
 cc: District File
 cc: Contractor

REMARKS / PROJECTED WORK

Prepared by: Brian Rodger
 Project Engineer

Approved _____, 2019

_____ Madison County

CONTRACTOR ACCEPTANCE

Primco, Inc.

PROJECT PHOTOS



Michiana installed the mass arms.



Michiana set the bridge poles.




Michiana installed the mass arms.



Michiana installed the light fixtures.

PROJECT PHOTOS

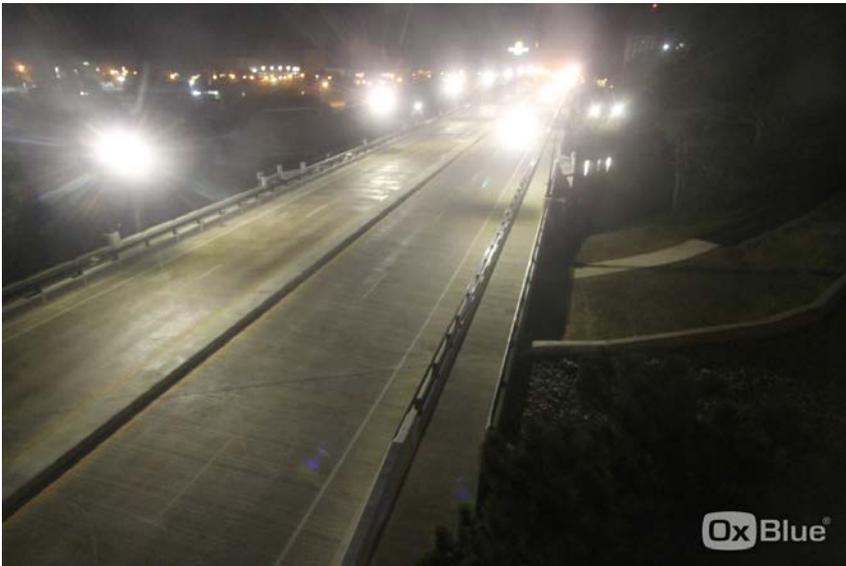

The completed bridge lighting.



The ribbon cutting ceremony.



The ribbon cutting ceremony.



The ribbon cutting ceremony.
